

01038/24

DATED

25 August

2024

SUFFOLK COUNTY COUNCIL (1)

- and -

BLOOR HOMES LIMITED (2)

- and -

SIR GEORGE ANTHONY AGNEW (3)

AGREEMENT

made pursuant to Sections 278 and 38 of the Highways Act 1980
and any other enabling power relating to
the development of land at Rougham Estate, Ipswich Road, Rougham, Bury St
Edmunds IP30 9LZ

Nigel Inniss
Head of Governance
Suffolk County Council
8 Russell Road Ipswich
Suffolk IP1 2BX

Ref: AS/72917/LEGAL

SECTION 278 AGREEMENT INDEX

	Page
Recitals & Definitions	
RECITALS AND DEFINITIONS.....	4
1 LEGAL EFFECT	9
2 NOTICES	9
3 GENERAL.....	10
4 ARBITRATION	11
5 COVENANTS.....	12
1 THE DESIGN OF THE HIGHWAY WORKS	15
2 LETTING OF THE CONTRACT.....	16
3 INSPECTION OF THE HIGHWAY WORKS	17
4 TESTING OF MATERIALS.....	18
5 OPENING OF THE HIGHWAY WORKS.....	19
6 UNDERTAKERS.....	20
7 PROTECTION OF THE PUBLIC	21
10 TIMING.....	23
11 SAFETY	23
12 ACCOMMODATION WORKS	24
13 CONSTRUCTION (DESIGN AND MANAGEMENT) REGULATIONS 2015	24
14 SITE CLEARANCE AND CERTIFICATE(S) OF SUBSTANTIAL COMPLETION	26
15 DEFECTS CORRECTION PERIOD AND CERTIFICATE OF FINAL COMPLETION	26

16	INDEMNITY	28
17	PERFORMANCE BOND / PERFORMANCE Cash deposit	29
18	COMMUTED SUMS FOR MAINTENANCE	30
19	LEGAL AND ADMINISTRATIVE COSTS	30
20	PARTS I AND II OF THE LAND COMPENSATION ACT 1973	32
	SCHEDULE II.A	33
	SCHEDULE II.B – <i>not used</i>	36
	SCHEDULE III	37
	SCHEDULE IV	38

THIS AGREEMENT is made the 5th day of August 2024
BETWEEN the following parties :-

- (1) **SUFFOLK COUNTY COUNCIL** of Endeavour House 8 Russell Road Ipswich
Suffolk IP1 2BX ("the County Council")
- (2) **BLOOR HOMES LIMITED** (company number 02162561) of Ashby Road,
Measham, Swandlincote, Derbyshire, DE12 7JP ("the Developer")
- (3) **SIR GEORGE ANTHONY AGNEW** of Rougham Estate Office, Ipswich Road,
Rougham, Bury St. Edmunds, IP30 9LZ ("the Owner")

RECITALS AND DEFINITIONS

(A) In this Agreement unless the context otherwise requires the following words
shall have the following meanings :-

"1980 Act"	Means the Highways Act 1980 (as amended)
"Approved Contractor"	Means the contractor(s) approved by the County Council for carrying out the Highway Works of the value and complexity proposed
"Approved Sub-Contractor"	Means the sub-contractor(s) approved by the County Council for carrying out the Highway Works of the value and complexity proposed
"CDM Regulations"	Means the Construction (Design and Management) Regulations 2015 (SI 2015/51)
"Certificate of Final Completion"	Means any of the certificates referred to in paragraph 15.3 of Schedule I
"Certificate of Substantial Completion"	Means any of the certificates referred to in paragraph 14.2 of Schedule I
"Commuted Sums"	Means the sum of £86,834.85 (Eighty Six Thousand, Eight Hundred and Thirty Four Pounds and Eighty Five Pence)

	which is calculated, as set out in paragraph 18.1 on Schedule I towards the cost of the County Council's future maintenance liability of the Highway Works
"Contract"	Means the contract or contracts in respect of each and all of the Highway Works
"Contractor"	Means the contractor or contractors who have been awarded the Contract to execute the Highway Works. For the avoidance of doubt the aforementioned definition does not include any subcontractor
"Development"	Means the development to be carried out pursuant to the Permission
"Director"	Means the County Council's Executive Director of Growth, Highways and Infrastructure or other officers of the County Council acting under his hand
"Highways England"	Means the body appointed by the Secretary of State for Transport as a strategic highways company under section 1 of the Infrastructure Act 2015 and statutory instrument 2015/376 or any other body so appointed
"Highway Works"	Means the works collectively or individually as the context requires which are set out in Schedule III of this Agreement and shown in the Works Drawings
"Highway Structure"	Means any bridge, subway, culvert, pipe, tunnel, or other structure built in, over, under or adjacent to any part of the highway
"Performance Bond"	Means the bond with the Performance Bond Surety for each and all of the Highway Works, such bond to be in the form set out in Schedule II.A, to the effect that should the Developer default in the execution of its obligations to carry out the Highway Works and to maintain the same in accordance with the provisions of this Agreement then the County Council will call upon the Performance Bond Surety to provide the full value of the Performance Bond (subject to the provisions

hereinafter contained) to carry out the Highway Works and maintain the same as aforesaid

"Performance Figure" Means the sum of £1,023,220.00 (One Million, Twenty-Three Thousand and Two Hundred and Twenty Pounds) being the Tender Sum plus 10 per cent in respect of the Highway Works and as set out in each of the Contracts

"Performance Bond Surety" Means National House-Building Council

"Permission" Means the planning permission granted by Babergh and Mid Suffolk District Council dated 23rd December 2020 granted with reference number DC/19/03486 in respect of the Site together with any modification of it

"Road Safety Audit" Means the evaluation of each and all of the Highway Works during design and at the end of construction to identify potential road safety problems that may affect any users of the highway and to suggest measures to eliminate or mitigate those problems in accordance with Department for Transport standards or by the County Council as agreed by the Director

"Site" Means at Rougham Estate, Ipswich, Road, Rougham, Bury St Edmunds IP30 9LZ edged red for identification only on the attached plan no PA590-EN-001 Rev A

"Specification" The County Council's "Specification for Estate Roads" dated May 2007 (or later amendment current at the date of this Agreement) so far as this is consistent with the Works Drawings and description in Schedule III (subject to any variations agreed in writing by the Director)

"Sub-contractor" Means the sub-contractor(s) working for the Contractor(s) who have been contracted to execute the Highway Works

"Substantial Completion" Means complete to the reasonable satisfaction of the Director and so that the Highway Works can be used for the purpose and operate in the manner for which they were designed

"Technical Standards"	Means the standards necessary to ensure complete conformity with all UK primary and secondary legislation (including by-laws) all guidance standards and codes of practice issued by the Department for Transport the County Council statutory undertakers and relevant professional institutes the Road Safety Audit and formal instructions issued by the Director from time to time during the design and implementation of the Highway Works and for the avoidance of doubt this shall include the Traffic Signs Regulations and General Directions 2016 and BS5489 in relation to the design of any street lighting
"Tender Sum"	Means the sum of £930,200.00 (Nine Hundred and Thirty Thousand and Two Hundred Pounds) (including the costs associated with statutory undertakers work and traffic management) agreed by the Director for carrying out the Contract by the Contractor
"Works Drawings"	Means the attached drawings bearing the numbers referred to in Schedule IV or any subsequent revision of them which has been approved or requested by the Director and which relate to the Highway Works

(B) In this Agreement unless the context otherwise requires :-

- (i) Words importing the singular meaning where the context so admits include the plural meaning and vice versa; and
- (ii) Words of the masculine gender include the feminine and neuter genders and words denoting actual persons include companies, corporations and firms and all such words shall be construed interchangeably in that manner; and
- (iii) "party" or "parties" means a party or parties to this Agreement; and
- (iv) references to any party shall include the successors in title and assigns of that party; and in the case of the County Council the successors to its statutory functions; and
- (v) where a party includes more than one person any obligations of that party can be enforced against all of them jointly and severally unless there is an express provision otherwise; and

- (vi) the headings and contents list in this Agreement shall not form part of or affect its construction; and
 - (vii) references to clauses schedules and paragraphs are references to clauses in and schedules to this Agreement and paragraphs in schedules to this Agreement; and
 - (viii) where a party or any officer or employee is required to give its consent approval or agreement to any specific provision in this Agreement such consent approval or agreement shall not be unreasonably withheld or delayed; and
 - (ix) any mention herein of any act or of any section regulation or statutory instrument shall be deemed to refer to the same source as at any time amended and where such act section regulation or statutory instrument has been replaced consolidated or re-enacted with or without amendment such mention shall be deemed to refer to the relevant provision of the updating consolidating or re-enacting act or section or regulation or statutory instrument
- (C) The County Council is the highway authority (except for trunk roads) for the purposes of the 1980 Act for the area within which the Site is situated and the Highway Works will be carried out
- (D) The Developer has the benefit of the Permission
- (E) The Owner is the registered proprietor with title absolute of part of the Site in so far as it is registered at the Land Registry under Title Number SK362697
- (F) The Owner wishes to dedicate as public highway that part of the Site upon which the Highway Works are to be constructed which does not currently form part of the public highway and the County Council agrees to accept such dedication and adopt that part of the Site and the Highway Works as highway maintainable at public expense on the terms and conditions hereinafter contained

- (G) Having regard to the development plan and other material considerations the County Council considers it expedient in the interests of the proper planning of their area that the Highway Works need to be carried out to facilitate the Development and that entering into this Agreement will be of benefit to the public

NOW THIS DEED WITNESSES as follows:-

1 LEGAL EFFECT

- 1.1. This Agreement and the covenants that appear hereinafter are made pursuant to Sections 38 72 and 278 of the 1980 Act Section 111 of the Local Government Act 1972 and Section 1 of the Localism Act 2011 and all other enabling powers to the intent that the provisions of this Agreement shall bind the Site and the parties hereto and all persons deriving title through or under them
- 1.2. This Agreement is a Deed. Any financial default under this Agreement will be registered as a Local Land Charge under section 278(5)(c) of the 1980 Act
- 1.3. No waiver (whether express or implied) by any party of any breach or default by the Developer in the performance or observance of any of the covenants, terms or obligations in this Agreement shall constitute a continuing waiver and no such waiver shall prevent the County Council from enforcing any of the covenants, terms or obligations or from acting upon any subsequent breach or default in respect thereof
- 1.4. Any provision of this Agreement which is or may be unlawful void or unenforceable shall to the extent of such unlawfulness invalidity or unenforceability be deemed severable and shall not affect any other provision of this Agreement
- 1.5. This Agreement is governed by and interpreted in accordance with English law and shall be determined in the Courts of England

2 NOTICES

- 2.1. Any notices or other written communication to be served or given by one party upon or to any other party under the terms of this Agreement

shall be deemed to have been validly served or given if delivered by hand or sent by recorded delivery post or sent by the DX service to the party upon whom it is to be served or to whom it is to be given or as otherwise notified for the purpose by notice in writing provided that the notice or other written communication is addressed and delivered by hand or by recorded delivery post or by the DX service to the address of the party concerned as nominated in sub-clause 2.2. below

- 2.2. The address for any notice or other written communication in the case of each party to this Agreement shall be as follows:-

The County Council	Suffolk County Council Endeavour House 8 Russell Road Ipswich IP1 2BX marked for the attention of the Assistant Director of Governance, Legal and Assurance (or where the context requires the Executive Director of Growth, Highways and Infrastructure, Endeavour House 8 Russell Road Ipswich IP1 2BX)
The Developer	marked for the attention of the Managing Director Bloor Homes Limited, Ashby Road, Measham, Swadlincote, DE12 7JP
The Owner	marked for the attention of the Owner and Estate Manager, Rougham Estate Office, Ipswich Road, Rougham, Bury St. Edmunds, IP30 9LZ

- 2.3. Any notice or other written communication to be given by the County Council shall be deemed to be valid and effective if on its face it is signed on behalf of the County Council by a duly authorised officer

3 GENERAL

- 3.1. All works and activities to be carried out under the terms of this Agreement (including for the avoidance of doubt such works as are of a preparatory ancillary or of a maintenance nature) are (save where

expressly provided otherwise) to be at the sole expense of the Developer and at no cost to the County Council

- 3.2. All consideration given and payments made in accordance with the provisions of this Agreement shall be exclusive of any VAT properly payable in respect thereof and in the event of VAT becoming chargeable at any time in respect of any supply made in accordance with the terms of this Agreement then to the extent that VAT had not previously been charged in respect of that supply the person making the supply shall raise a VAT invoice to the person to whom the supply was made and the VAT shall be paid accordingly
- 3.3. The County Council and their respectively duly authorised officers and agents may enter upon the land on which the Highway Works are being carried out at any reasonable time to ascertain whether the terms of the Agreement are being or have been complied with
- 3.4. The Owner enters into this Deed solely for the purposes of dedicating land as new public highway in accordance with the terms of the paragraphs 14.3 and 15.4 of the Schedule and to provide the covenant at clause 5.1 and shall incur no other liability whatsoever under the terms of this Deed

4 ARBITRATION

- 4.1. Any dispute or difference arising between the parties as a result of this Agreement may be referred to the arbitration of a single arbitrator to be agreed upon between the parties or failing agreement within fourteen days after either of the parties has given to the other a written request requiring the appointment of an arbitrator to a person to be appointed at the request of either of the parties by the President for the time being of The Institution of Civil Engineers
- 4.2. Any reference to arbitration shall be undertaken in accordance with and subject to the provisions of the Arbitration Act 1996 save as follows:-
 - (a) the seat of the arbitration shall be at the County Council's offices in Ipswich Suffolk

- (b) where appropriate the arbitrator may consolidate arbitral proceedings
 - (c) with the parties' agreement the arbitrator may appoint experts or legal advisers
- 4.3 A party wishing to refer any such dispute or difference to arbitration shall notify the other party in writing of such intention without delay
- 4.4 The arbitrator shall act as a referee and not as an expert except in any case where the parties to a dispute or difference agree on the arbitrator when such parties may also agree that such arbitrator shall act as an expert
- 4.5 Subject to Sections 67 68 and 69 of the Arbitration Act 1996 the parties agree to be bound by the decision of the arbitrator

5 COVENANTS

- 5.1 The Owner covenants and warrants to the County Council that they have full power to enter into this Agreement and there is no other person having a charge over or any other interest in the Site whose consent is necessary for the Owner to enter into this Agreement and to comply with the obligations set out at paragraph 14.3 of Schedule I
- 5.2 The Developer hereby covenants and undertakes with the County Council that from the date of this Agreement it will (unless otherwise agreed by the County Council) carry out and comply with the obligations set out in Schedule I and the details set out in Schedules III and IV hereto
- 5.3 The County Council without prejudice to its statutory powers and duties hereby appoints the Developer to act as its agent and gives to the Developer licence (in so far as is reasonably necessary for the Developer to perform the obligations under the terms of this Agreement) to enter into and upon and remain upon the highway to carry out the construction of the Highway Works within the timescales referred to in Schedule III hereto or such other period as may be agreed in writing by the Director, provided that this licence shall not extend to the Developer's successors in title or assigns unless otherwise agreed in writing by the Director prior to that successor or assignee commencing work in the public highway

- 5.4 The Developer covenants with the County Council not to commence the Highway Works set out in Schedule III unless road space has first been booked with the County Council and Highways England
- 5.5 The Developer covenants with the County Council as highway authority to give written notice not less than three calendar months prior to works commencing, in order that the County Council as highway authority has sufficient time to ensure that the commencement of works will cause the least disruption possible to road users and the County Council reserves the right to refuse consent and/or to stop or require the stopping of works under the terms of this Agreement and relevant legislation where the aforesaid notice period is not complied with
- 5.6 The Developer covenants with the County Council as highways authority to comply with the provisions of the New Roads and Street Works Act 1991, the Traffic Management Act 2004 and any amendments thereof
- 5.7 The County Council covenants with the Developer that on the date of issue of the Certificate of Final Completion the roads subject to the Highway Works shall thenceforth be, to the extent they are not already, adopted as highways maintainable at the public expense

6 THIRD PARTY RIGHTS

- 6.1 It is hereby agreed and declared that the provisions of Contracts (Rights of Third Parties) Act 1999 shall not apply to this Agreement

7 LAPSE

- 7.1 If the Highway Works have not been commenced within one (1) year from the date of this Agreement, save as this period is otherwise extended in writing by the Director at his discretion, then this Agreement shall lapse and be of no further effect (save to the extent already complied with) and the Developer agrees to pay to the County Council any costs properly incurred by the County Council prior to the lapse of this Agreement (which have not already been paid) including but not limited to those costs set out in paragraph 19 of Schedule I to this Agreement
- 7.2 Where, in accordance with clause 7.1 above the Director, at his discretion, agrees in writing to an extension to the period of one (1) year

after which this Agreement shall lapse, this Agreement shall lapse at the end of such period as agreed in writing by the Director where the Highway Works have not been commenced by the expiry of that extension period

In witness whereof this Agreement has been executed and delivered as a Deed on the date first written above

The COMMON SEAL of)
SUFFOLK COUNTY COUNCIL)
was hereunto affixed)
in the presence of)



[Redacted signature block]

A Duly Authorised Officer

EXECUTED AS A DEED by SIR GEORGE ANTHONY AGNEW
in the presence of:

Witness signature:

Name:

Address:

EXECUTED AS A DEED by BLOOR HOMES LIMITED
acting by [Redacted] a director, in the presence of [Redacted]

Authorised Signatory

Director:

Director/Secretary:

Witness

[Redacted signature block]

[Redacted signature block]

[Redacted signature block]

SCHEDULE I

1 THE DESIGN OF THE HIGHWAY WORKS

- 1.1 The design of the Highway Works shall be to the satisfaction of the Director with due consideration of the Technical Standards
- 1.2 No work on any of the Highway Works shall commence and no Contract for their construction shall be let until
 - 1.2.1 full details of the design of the Highway Works to be commenced in the form of plans, drawings, specifications and other materials have been submitted to the Director together with the name of the principal designer (whom the Developer shall appoint for the full duration of the design and construction of each and all of the Highway Works) in accordance with the CDM Regulations and any codes of practice referred to therein
 - 1.2.2 the Director has given his written approval to the Highway Works to be commenced and such approval shall not be given if the said plans, drawings, specifications and other documentation have not adequately addressed the issues raised in the pre-construction stages of the Road Safety Audit process and if given shall lapse if the Highway Works are not commenced within twelve (12) months of the date of the said Director's approval
 - 1.2.3 preliminary proposals, detailed contract drawings, schedules and specifications for Highway Structures have been prepared by the Developer and submitted for written approval to the Director's Bridge Office in accordance with Department for Transport Document BD2/12 and the structural design and checking procedure has been carried out by an incorporated or chartered engineer familiar with Department for Transport Codes of Practice and experienced in the design of Highways Structures. The documents are to be agreed as applicable with the Director before the design is commenced and details are submitted for approval

- 1.3 If the Director does not propose to give his approval in relation to those matters referred to in paragraph 1.2 of this Schedule he shall in each case as soon as possible in writing inform the Developer and if the Director requires amendments or additions to the plans drawings specifications and other materials referred to in paragraph 1.2 of this Schedule these amendments shall be undertaken by the Developer at his own expense and a revised set of updated documents shall be re-submitted to the Director for his approval
- 1.4 Without prejudice to paragraph 1.2 of this Schedule, the Director shall not give his approval as referred therein until the Developer has paid the sum referred to in paragraph 19.1.3 towards the cost of checking the design of the Highway Works and inspecting the Highway Works. The Highway Works at all times shall be carried out in accordance with the plans, drawings, specifications and other materials which have received the Director's approval referred to in paragraph 1.2 of this Schedule and the Developer shall in the execution of the Highway Works comply or ensure that the Contractor complies with the Technical Standards

2 LETTING OF THE CONTRACT

- 2.1 No Contract shall be let until all traffic management measures have been prepared by the Developer and approved in writing by the Director ("the approved programme") and thereafter each of the Contracts will be offered to an Approved Contractor
- 2.2 The Contract to be let under paragraph 2.1 of this Schedule shall be let under NEC3 suite of contracts (and any amendments thereto shall be approved by the Director) and the Developer shall obtain the agreement of the Contractor to be bound by the agreed drawings in Schedule IV
- 2.3 The Contract shall be awarded by the Developer subject to the Director having first given his written approval to the proposed chartered engineer(s) or other suitably qualified person(s) who shall be independent of the Contractor and will supervise the execution of the Highway Works by the Contractor
- 2.4 The Developer shall not award the Contract unless the Approved Contractor and the Approved Sub-Contractor/s concerned are insured throughout the period of the Contract (such period to include the

maintenance period detailed in paragraph 15.1 of this Schedule) for public liability risks in the sum of at least ten million pounds (£10,000,000) in respect of any single claim and the Developer shall ensure that the Contractor remains so insured throughout the period of the Contract and prior to the commencement of each or all of the Highway Works or any maintenance works carried out in accordance with paragraph 15.1 of this Schedule the Developer shall produce to the Director insurance policies fully covering the Developer's liability in respect of the matters set out in this Agreement

- 2.5 The Developer shall not sub-contract or assign the Contract without the written approval of the Director and any sub-contractor shall be an Approved Sub-Contractor

3 INSPECTION OF THE HIGHWAY WORKS

- 3.1 The Developer shall provide the Director with not less than twenty-four (24) hours nor more than seventy-two (72) hours notice (excluding weekends and bank holidays) of any intended execution of the Highway Works specifying the tasks to be carried out in accordance with the approved programme referred to in paragraph 2.1 of this Schedule
- 3.2 Without prejudice to the approved programme the Developer shall notify the Director in writing at least twenty-eight (28) days prior to the commencement of any work connected with statutory undertaker's equipment
- 3.3 Without prejudice to the approved programme the Developer shall notify the Bridge Office and the Director in writing at least seventy-two (72) hours prior to the commencement of each and every stage of excavation and concrete operations associated with any Highway Structures
- 3.4 The Developer shall during the progress of each and all of the Highway Works give to or procure for the Director and any person or persons duly authorised by him free access to every part of the Highway Works and the Site and permit him or them to inspect the same as they proceed and all materials used or intended to be used therein and shall give effect to any reasonable and proper requirements made or reasonable and proper directions given by the Director to conform to the approved detailed plans

Works Drawings and specification referred to in paragraph 1.2 of this Schedule

- 3.5 The Developer shall not cover up or put out of view any works forming part of the Highway Works without the approval of the Director and shall afford full opportunity for the Director to examine and measure any work which is about to be covered up or put out of view and to examine foundations before permanent work is placed thereon and shall give at least seventy-two (72) hours' notice to the Director whenever any such work or foundations is or are ready or about to be ready for examination
- 3.6 The Director shall without unreasonable delay, unless she considers it unnecessary and advises the Developer accordingly, attend when required by the Developer for the purpose of examining such works or of examining such foundations
- 3.7 The Director shall for the purposes of paragraphs 3.1 to 3.6 be allowed reasonable access and admission to the Highway Works or the places where materials or plant for the Highway Works may be stored or in the course of preparation manufacture or use (unless such access or admission is refused due to circumstances beyond the control of the Developer)

4 TESTING OF MATERIALS

- 4.1 The Developer shall reimburse the County Council for all reasonable costs and expenses whatsoever arising from the operation of paragraphs 4.2 to 4.5
- 4.2 The Director shall require the testing of materials plant and workmanship used or proposed to be used in the Highway Works and in his reasonable discretion have the power to reject any materials plant or workmanship so tested which he may reasonably and properly find to be not in accordance with the approved detailed plans Works Drawings and specification referred to in paragraph 1.2 of this Schedule In relation to Highways Structures the Director will require a schedule of testing to be agreed prior to the commencement of works or any part thereof
- 4.3 The Developer shall as soon as is reasonably practicable replace or repair any materials plant or workmanship which have been found to be

not in accordance with the approved detailed plans Works Drawings and specification referred to in paragraph 1.2 of this Schedule

4.4 The Director shall for the purposes of paragraphs 4.2 to 4.5 be allowed reasonable access and admission to the Highway Works or the places where materials or plant for the Highway Works may be stored or in the course of preparation manufacture or use (unless such access or admission is refused due to circumstances beyond the control of the Developer)

4.5 The Developer shall as soon as is reasonably practicable remove such materials and plant as are rejected by the Director pursuant to paragraph 4.2. of this Schedule which are not capable of repair or remedy from the Site and if the Developer shall wish to continue to store such rejected materials and plant on the Site they shall be stored separately from those materials and plant which have not been so rejected or which the Developer shall wish in future to use in execution of the Highway Works

5 OPENING OF THE HIGHWAY WORKS

5.1 During the construction of each and all of the Highway Works and prior to the issue of the Certificate of Substantial Completion:

- (a) the Director may issue instructions to the Developer to open or expose any of the Highway Works which has been covered up without previously being inspected by the Director
- (b) should the Developer fail to comply with any such instructions the County Council may so take up or expose the relevant part of the Highway Works causing as little damage or inconvenience as is possible in respect of any other part or parts of the Highway Works the reasonable and proper cost of such taking up or exposure and reinstatement to be met by the Developer

PROVIDED THAT if the Highway Works or any part or parts thereof are covered up by the Developer after giving the notice referred to in paragraph 3.5 of this Schedule and the Director shall have failed to inspect in the period therein referred to and the Director shall subsequently require the Highway Works or any part of them to be uncovered for the purposes of inspection:-

- (a) if inspection reveals the relevant part or parts of the Highway Works to have been completed in accordance with the approved detailed plans drawings and specification referred to in paragraph 1.2 of this Schedule all costs in respect of such uncovering and inspection and of reinstating the part or parts of the Highway Works uncovered shall be borne by the County Council; or
- (b) if inspection reveals the relevant part or parts of the Highway Works not to have been completed in accordance with the approved detailed plans drawings and specifications referred to in paragraph 1.2 of this Schedule all reasonable and proper costs in respect of uncovering and inspection and of reinstating the part or parts of the Highway Works uncovered shall be borne by the Developer

6 UNDERTAKERS

6.1 Insofar as the County Council as Highway Authority is required by any legislation regulation direction or code of practice (including in particular but without prejudice to the generality of the foregoing the New Roads and Street Works Act 1991) to serve a notice or notices in respect of the Highway Works on undertakers or other persons the Developer shall comply with such requirement on behalf of the County Council before the Highway Works commence and shall thereafter assume on behalf of the County Council such responsibilities as follow on therefrom in particular during the construction of the Highway Works and prior to the issue of the Certificate of Substantial Completion the Developer shall also:-

- (a) carry out or procure the carrying out of such works and activities in regard to the plant and equipment of undertakers as are required by undertakers in accordance with their statutory powers under the New Roads and Street Works Act 1991 as a result of the construction or intended construction of each and all of the Highway Works
- (b) cause all public sewers, highway drains gas and water mains electric cables and telecommunications ducts or other apparatus which are to be laid by the Developer under the Highway Works together with all necessary connections from them to the boundary of the Highway Works to be laid so far as is practicable under the

Highway Works before the foundation of the Highway Works are laid and shall also in so far as is practicable cause the connections from electric cables to any street lamp to be laid before the paving of the footways comprised in the Highway Works is carried out

- (c) cause all trench works within the highway to be backfilled and reinstated in accordance with the Specification for the Reinstatement of Openings in the Highway as determined from time to time under the New Roads and Street Works Act 1991
- (d) not at any time give consent to the erection by any telecommunications operator of telegraph poles or telephone poles or to the erection by any statutory undertaker or public or private company firm or individual of any over ground or underground equipment without the consent in writing of the Director

7 PROTECTION OF THE PUBLIC

- 7.1 The Developer shall give due consideration to adjoining owners and occupiers at all times and shall organise activities relating to the Highway Works in such a manner as to cause the least practicable disruption
- 7.2 Prominent notices shall be displayed and maintained around the perimeter of the site of each and all of the Highway Works to warn the public of the dangers of entering the Site
- 7.3 The Developer shall nominate a member of the site management team as the contact point for the Director in the event of an emergency and shall advise a daytime and twenty-four (24) hour contact number to the Director for the same purpose
- 7.4 The Developer shall take or procure the taking of all necessary steps to avoid creating a nuisance from noise and in particular:
 - 7.4.1 the Developer shall afford all reasonable facilities to enable the Director to carry out such site investigations as she may deem necessary in order to determine noise emission levels
 - 7.4.2 all vehicles and plant including compressors shall be fitted with effective silencers and acoustic covers as appropriate and maintained in good working order and all static plant shall be

located to minimise nuisance to persons living or working in the vicinity

7.4.3 all portable traffic signals and pumps shall be operated from mains electricity unless otherwise agreed with the Director

7.4.4 noisy activities shall not be permitted on Sundays and Bank Holidays and except as agreed in writing by the Director shall not be permitted outside the hours of 9.30 a.m. to 4.30 p.m. Monday to Friday and 9.30 a.m. to 1 p.m. on Saturdays

PROVIDED THAT if in the reasonable opinion of the Director the Developer is not dealing adequately with the control of noise the Developer shall carry out or procure the carrying out of such additional measures as the Director considers necessary at the Developer's expense

7.5 Compliance with the provisions of paragraph 7.4 shall not relieve the Developer of any of his obligations and liabilities under this Agreement the Control of Pollution Act 1974 or the Environmental Protection Act 1990

7.6 The Developer shall take or procure the taking of all necessary steps to avoid creating a nuisance from dust and as far as practicable works are to be carried out in such a way that dust is kept to a minimum PROVIDED THAT if in the reasonable opinion of the Director the Developer is not dealing adequately with the control of dust the Developer shall carry out or procure the carrying out of such additional measures as the Director considers necessary at the Developer's expense

7.7 The Developer shall arrange the regular removal of refuse likely to encourage vermin and arrange for suitable secure storage containers to be provided for collection

7.8 The Developer shall keep a log book on site to record all complaints received from the public and the action taken in response and the log book shall be available for inspection by the Director

8 PREVENTION OF MUD BEING CARRIED ON THE PUBLIC HIGHWAY

8.1 Provision shall be made at the Site to limit in so far as is practicable the amount of mud dust and other materials carried on to adjacent public highways by vehicles and plant leaving the Site

8.2 The Developer shall keep or procure the keeping of all roads footpaths rights of way and other means of passage leading to or from or crossing the Site free from mud slurry or other hazardous substances that are deposited through the construction of the Highway Works and any such substance so deposited on any such road footpath right of way or other means of passage shall be promptly removed by or at the direction of the Developer

8.3 The Director may close any associated crossings entrances and exits if such substances deposited are not promptly removed by the Developer and any losses or expenses incurred as a result shall be borne by the Developer and on removal of such substances the Director shall reopen such crossings entrances and exits and the Developer shall bear the costs incurred

9 TRAFFIC CONTROL

9.1 During the periods when the Highway Works are being executed the Developer shall institute at his own expense measures previously approved in writing by the Director to maintain the safe flow of traffic on the highways in the vicinity of the site of the Highway Works

9.2 The Highway Works shall be signed and protected to at least the standards of Chapter 8 of the Traffic Signs Manual published by His Majesty's Stationery Office and the proposed arrangements shall be approved in writing by the Director before the Highway Works commence

10 TIMING

10.1 No Highway Works within or affecting existing public highways or temporary diversions which could interfere with the traffic flow will be permitted within the morning and evening peak periods i.e. 7.30 - 9.30 a.m. and 4.30 - 6.30 p.m. Monday to Friday except as agreed in writing by the Director

11 SAFETY

11.1 During the periods when the Highway Works are being carried out the Developer shall provide all watching and lighting as required and shall maintain all lights, guards, fencing, warning signs when and, where necessary, undertake such further measures as may be reasonably required by the Director

12 ACCOMMODATION WORKS

12.1 The Developer shall carry out or ensure that there shall be carried out all related accommodation works associated with the Highway Works

13 CONSTRUCTION (DESIGN AND MANAGEMENT) REGULATIONS 2015

13.1 The Developer shall be the only client for the purpose of the CDM Regulations and the Developer agrees to undertake the obligations of a client under the CDM Regulations and to use all reasonable endeavours to ensure that the Highway Works are carried out in accordance with the CDM Regulations

13.2 The Highway Works shall not commence until the Developer as the only client has provided to the Director:

13.2.1 an estimate of the number of working days and/or person days of construction work and the number of workers working on site simultaneously at any one point in the project which the Contract will entail

13.2.2 written details of the principal designer and the principal contractor appointed for the project and also provide copies of the Construction Phase Plan and Health & Safety File

13.2.3 a copy of the Notification of Project (form HSE F10) to the HSE pursuant to Regulation 6 of the CDM Regulations

13.3 Throughout the Highway Works the Developer shall provide to the Director copies of the updates and revisions to the construction phase plan and Health and Safety File pursuant to Regulation 12

13.4 Within twenty-eight (28) days of issue of the Certificate of Substantial Completion for any or all of the Highway Works the Developer shall provide to the Director

- 13.4.1 a plan showing the land over which those Highways Works have been constructed and
 - 13.4.2 a Health and Safety file conforming in all respects with the CDM Regulations and which shall accord with the current format used by the County Council to include a separate Health and Safety File for each Highway Structure
- 13.5 The Director shall be at liberty to delay issue of the Certificate of Final Completion in respect of any of the Highway Works if the Developer fails to provide the Director with the documents referred to in 13.4.1 and 13.4.2 above within twenty-eight (28) days of issue of any Certificate of Substantial Completion for any of the Highway Works equivalent to the number of days after the twenty-eight (28) day period that the documents were submitted
- 13.6 In respect of the Highway Works generally the Developer shall provide to the Director the final information in both paper and electronic format and shall at least comprise:
- 13.6.1 1:500 scale (or alternative scale as may be specified by the Director) "as built" drawings
 - 13.6.2 records of the earthworks showing sources of material used in areas of fill description of fill materials descriptions of sub-grades in cut areas copies of results of tests of material carried out as part of the supervision of the construction of the earthworks
 - 13.6.3 records of the sources of supply of all deliveries of road construction materials with details of the location of the Highway Works at which each load is placed
 - 13.6.4 records of the sources of supply of all other manufactured materials (e.g. drainage goods, fencing materials, traffic signs, electrical components and cables etc).
- 13.7 No work on Highway Structures shall commence until the general Health and Safety file information including format to be supplied in respect of Highway Structures has been agreed with the County Council's Bridge Engineer and shall accord with the County Council's current Technical

Approval Procedure for Highway Structures

- 13.8 The Developer shall indemnify and keep the County Council indemnified against any breach of the Developer's obligations under this paragraph 13

14 SITE CLEARANCE AND CERTIFICATE(S) OF SUBSTANTIAL COMPLETION

- 14.1 On Substantial Completion of the Highway Works the Developer shall:-

14.1.1 clear away and remove from the site of the Highway Works all constructional plant and temporary works of every kind and leave the site of the Highway Works in a neat and tidy condition to the satisfaction of the Director and

14.1.2 carry out stage 3 of the Road Safety Audit process and comply to the satisfaction of the Director with recommendations arising thereunder prior to the opening of the Highway Works to the public

- 14.2. Upon Substantial Completion of the Highway Works including any additional work resulting from stage 3 of the Road Safety Audit process to the satisfaction in all respects of the Director he shall issue a Certificate of Substantial Completion in respect of those Highway Works to the Developer provided that all costs and expenses owing to the County Council have been paid in respect of those Highway Works

- 14.3. The First Owner hereby agrees that on the date of Substantial Completion that part of the Site upon which the Highways Works are constructed which does not currently form part of the public highway shall be dedicated as highway under section 38 of the 1980 Act

- 14.4. After the issue of the Certificate of Substantial Completion the County Council may approve a reduction of up to 90% of the Performance Figure in respect of the relevant Highway Works and the County Council may release the Developer and the Performance Bond Surety and each of them from their obligations under the Performance Bond in respect of the relevant Highway Works to such extent

15 DEFECTS CORRECTION PERIOD AND CERTIFICATE OF FINAL COMPLETION

- 15.1 The Developer shall maintain each and all of the Highway Works for a period of eighteen (18) months (unless the Director agrees in writing a lesser period having considered paragraph 15.2) from the issue of the related Certificate of Substantial Completion and prior to the expiration of this period the Developer shall reinstate and make good any damage or defect which may have arisen from any cause whatsoever or be discovered during the said period of eighteen months (including any defect in or damage to the surface water drainage system) so as to place the highway and the Highway Works in a condition satisfactory to the Director
- 15.2 After the expiration of the period of twelve (12) months from Substantial Completion or the date the Development becomes operational (whichever is the latter) the Developer shall (unless the Director writes to the Developer informing him that it is to be carried out sooner or that he does not need to do so) carry out stage 4 of the Safety Audit and comply to the satisfaction of the Director with any recommendations arising thereunder
- 15.3 After the expiration of the period of eighteen (18) months referred to in paragraph 15.1 (or such lesser period as agreed in writing by the Director under paragraph 15.1) and after any defects have been made good as therein provided including any improvements arising under stage 4 of the Road Safety Audit to the satisfaction of the Director and after the provisions of paragraph 13.4 and paragraph 20.2 of this Schedule have been fulfilled the Director shall issue forthwith to the Developer the Certificate of Final Completion in respect of the Highway Works provided that the Certificate of Final Completion shall in the case of road gullies extend only as far as their points of entry to the surface water sewers where those are not being adopted by the County Council as highway drains and upon the issue of the Certificate of Final Completion the County Council shall release the Developer and the Performance Bond Surety and each of them from all subsisting obligations under the Performance Bond in respect of those Highway Works
- 15.4 If called upon to do so by notice in writing served within twenty-one years of the date hereof by the County Council the Owner agrees to transfer to the County Council in consideration of one pound any land over which

any part of the Highway Works have been constructed which does not at the date of this Agreement already form part of the highway together with any other land dedicated as public highway by the Owner hereunder free in each case from encumbrances and together with all rights necessary to permit the use inspection maintenance repair and replacement of all utility systems servicing the Highway Works and not vested in the relevant undertaker as are situated outside the limits of the Highway Works and the said other land

16 INDEMNITY

16.1 The Developer shall from the date of this Agreement indemnify the County Council against all claims charges costs expenses liability or loss whatsoever arising out of and incidental to any or all of the Highway Works including but not limited to those arising out of any legally sustainable claims for payments under Section 10 of the Compulsory Purchase Act 1965 and Part I of the Land Compensation Act 1973 (as amended) in connection with those Highway Works provided that the Developer's indemnity will not extend to any claims submitted to the County Council arising out of the negligence of the County Council's employees or arising out of any works of alteration carried out to any of the Highway Works by the County Council after the issue of the related Certificate of Final Completion

16.2 The County Council shall notify the Developer forthwith upon receipt of any such claim or liability

16.3 The County Council shall not accept or settle any claim without first having given the Developer the opportunity to provide the County Council with representations as to the validity of such claim

16.4 The indemnification referred to in paragraph 16.1 includes:

16.4.1 all fees incurred by claimants which the County Council is obliged to pay, and those of the County Council or its agent or contractor, in negotiating any claims (together with VAT payable on the claimants' professional advisors' fees);

16.4.2 statutory interest payments to claimants and their professional advisors; and

16.4.3 the County Council's reasonable and proper legal costs in making the compensation, fees and interest payments

17 PERFORMANCE BOND

17.1 Without expense to the County Council the Developer and the Performance Bond Surety shall on the date of this Agreement enter into the Performance Bond for each and all of the Highway Works and the Developer and Performance Bond Surety shall be bound to the County Council in the amount of the Performance Figure for the Highway Works

17.2 Should the Developer default in the execution of its obligations to carry out any or all of the Highway Works and to maintain the same in accordance with the provisions of this Agreement then the County Council may (subject to the provisions hereinafter contained) itself carry out the Highway Works and maintain the same as aforesaid having first called upon the Performance Bond Surety for the cost to be expended in so doing

17.2.1 Unless there is a danger to users of the highway the County Council shall give twenty (20) working days prior written notice (or lesser period as may in the circumstances be reasonable) of its intention to commence work under Paragraph 17.2

17.2.2 any notice served under this paragraph shall specify the period of the notice ("the Notice Period") the extent of the work which the County Council proposes to carry out and full details of all matters in respect of which the Director considers that the Highway Works have not been carried out in accordance with the terms of this Agreement

17.2.3 if before the expiry of the Notice Period the Developer serves written notice upon the County Council that the Developer intends diligently to execute the works specified in the notice in accordance with the terms of this Agreement and specifies a time to complete that the County Council considers reasonable in the circumstances the County Council shall not be entitled to execute the relevant part or parts of the Highway Works specified in the notice served under this paragraph unless the

Developer then fails to execute those works within the agreed time scale

17.3 If the Developer should default in the execution of its obligations to carry out any or all of the Highway Works and to maintain the same in accordance with the provisions of this Agreement then the County Council will call upon the Performance Bond Surety to provide the full Performance Figure (or such sum that remains following reduction of the Performance Bond in accordance with Paragraph 14.4 of this Schedule) in accordance with this Agreement. Save that the County Council after all works are completed and all contracts and any contract claims settled will return any Performance Bond sum unused with interest at the Bank of England Base Rate minus 2 basis points, compounding annually at financial year end on receipt of a written request to the Performance Bond Surety within one month of all the aforementioned completing and settling. If for any period the Bank of England Base Rate is at or below 0.02% then no interest shall be payable for that period by any party to this Agreement

18 COMMUTED SUMS FOR MAINTENANCE

18.1 Prior to the date of this Agreement the Developer shall pay to the County Council the Commuted Sums calculated as follows:

	£
Roads	54,602.30
Footways	2,884.05
Street Lighting	21,695.50
Drainage	7,025.00
Traffic Signals	628.00

19 LEGAL AND ADMINISTRATIVE COSTS

19.1 The Developer shall pay to the County Council:-

- 19.1.1 the whole of the costs of the County Council's Legal Services Department in connection with the preparation and completion of this Agreement and these costs shall be payable prior to sealing of this Agreement;
- 19.1.2 interest at four per cent above the Bank of England Base Rate from time to time on any sum due to the County Council under this Agreement which is outstanding for more than twenty-eight (28) days from the date on which it was demanded or in the event that a dispute or difference regarding such payment is referred to arbitration pursuant to clause 4.1 of this Agreement the said twenty-eight (28) day period shall run from the date of the decision of the arbitrator (such interest to be charged on the amount outstanding each day from the date of issue of a written demand for any sum due or in the event that a dispute or difference regarding such payment is referred to arbitration pursuant to clause 4.1 of this Agreement such interest to be charged on the amount outstanding each day from the date of issue of the decision of the arbitrator)
- 19.1.3 The greater of £5000 (Five thousand pounds) or 7½% of the Performance Figure (excluding the costs associated with statutory undertakers work and traffic management) for the Highway Works towards the costs and expenses of the County Council of checking the design of each and all of the Highway Works and inspecting each and all of the Highway Works such sum shall be payable prior to sealing of this Agreement
- 19.1.4 the reasonable cost to the County Council of undertaking Road Safety Audits and also the cost of the safety checks of details submitted which sum shall be payable prior to the safety audit commencing
- 19.1.5 the cost of any temporary and permanent traffic regulation orders which sum shall be payable prior to any work on the making of such order being commenced

19.1.6 the full cost of any other road traffic orders required to facilitate the Highway Works which sum shall be payable prior to any work on the making of such order being commenced

19.1.7 In cases where it may be necessary to enter into a Section 4 or 6 agreement under the Highways Act 1980, the cost of inspecting each and all of the Highway Works on behalf of Highways England, the cost of checking the design of each and all of the Highway Works on behalf of Highways England, the cost of any Highways England fees, and the reasonable cost of County Council administrative and legal fees, which sums shall be payable prior to the sealing of this Agreement

20 PARTS I AND II OF THE LAND COMPENSATION ACT 1973

Part I and II Claims

Part I Claims - Depreciation Caused By Public Works

20.1 The Developer hereby undertakes and agrees with the County Council that in the event of any claim for compensation or otherwise or costs or charges arising in connection with or incidental to or in consequence of the carrying out of the Highway Works whether mandatory or discretionary which may be incurred by virtue of any enactment or statutory instrument and otherwise hereby provided for he will hold the County Council fully indemnified from and against all claims charges costs and expenses in connection therewith or arising therefrom

Part II Claims

20.2 The Developer covenants with the County Council to comply with the requirements of the Noise Insulation Regulations 1975 (SI 1975/1763) as amended and to provide to the County Council such evidence as is required by the Director to demonstrate compliance with the Noise Insulation Regulations 1975 prior to the issuing by the County Council of the Certificate of Final Completion in accordance with paragraph 15.3 of this Schedule

SCHEDULE II.A

Performance Bond Agreement

DATED

5 August

2024

BLOOR HOMES LIMITED (1)


- and -

NATIONAL HOUSE-BUILDING COUNCIL (2)

PERFORMANCE BOND

relating to the development of land at Rougham Estate, Ipswich Road, Rougham,
Bury St Edmunds IP30 9LZ Suffolk

BY THIS BOND **BLOOR HOMES LIMITED** of Ashby Road, Measham, Swandlincote, Derbyshire, DE12 7JP ("the Developer") and

 NATIONAL HOUSE-BUILDING COUNCIL ("the Surety") are held and firmly bound of NHBC House, Oakley Avenue, Knowlhill, Milton Keynes, MK5 8FP to **SUFFOLK COUNTY COUNCIL** of Endeavour House 8 Russell Road Ipswich Suffolk IP1 2DH ("the County Council") in the sum of £1,023,220.00 (One Million, Twenty Three Thousand and Two Hundred and Twenty Pounds) to be paid to the County Council for the payment of which sum the Developer and the Surety bind themselves their successors and assigns jointly and severally

IN WITNESS whereof the Developer and the Surety have hereunto executed and delivered the same on but not before this 5th day of August Two thousand and Twenty-Four

1. The Developer has entered into an Agreement under seal with the County Council of even date made under Section 278 of the 1980 Act whereby the Developer undertook at its own expense to carry out works as set out in Schedule III of the said Agreement and shown in the Works Drawings annexed to the said Agreement ("the Highway Works")
2. It is intended that this Bond shall be construed as one with the said Agreement

NOW THE CONDITION of the above-written Bond is such that if the Developer shall duly perform and observe all the terms provisions conditions and stipulations of the said Agreement (in so far as they relate to the Highway Works) on the Developer's part to be performed and observed according to the true intent and meaning thereof or if on default by the Developer the Surety shall duly satisfy and discharge the damages sustained by the County Council up to the amount of the above-written

Bond then the above-written Bond shall be null and void but otherwise shall remain in full force and effect **PROVIDED ALWAYS** that the giving by the County Council of any extension of time for performing the said Agreement or any stipulations therein contained and on the part of the Developer to be performed or any other forgiveness or forbearance on the part of the County Council or its successors or assigns shall not in any way release the Surety from any liability under the above-written Bond

EXECUTED AS A DEED by BLOOR HOMES LIMITED
acting by a director, in the presence

Witness

Director:

Director/Secretary:

Signed as a deed by [redacted] as attorney for
National House-Building Council under a Power of Attorney
dated [23rd May 2024]

Project Underwriter

As attorney for National House-Building Council

In the presence of:

Name of Witness

Witness Signature

Occupation of Witness

Address of Witness

SCHEDULE II.B – *not used*

SCHEDULE III

The Highways Works comprising the following works:


<u>Location</u>	<u>Works</u>	<u>Delivery Programme</u>
Fishwick Corner, Barton Road/Mount Road Junction, Thurston	Junction improvements at Fishwick Corner changing a crossroads into a staggered junction.	
Mount Road, Thurston	New residential access into development site and minor highway improvements	

Timescales: The Highways Works are to be commenced within 12 (twelve) months of the date of this Agreement and completed within 3 (three) months of commencement of the Highway Works

SCHEDULE IV

Approved List of drawings

	Title	Drawing number
1.	S278 LOCATION PLAN	PA590-EN-001A
2.	S278 FISHWICK CORNER GA SHEET 1	PA590-EN-331A
3.	(S278 FISHWICK CORNER GA SHEET 2)	PA590-EN-332A
4.	(S278 FISHWICK CORNER ROAD SETTING OUT)	PA590-EN-333A
5.	(S278 FISHWICK CORNER ROAD LONG SECTIONS)	PA590-EN-334A
6.	(S278 FISHWICK CORNER LAND DEDICATION)	PA590-EN-335A
7.	(S278 FISHWICK CORNER CONSTRUCTION DETAILS SHEET 1)	PA590-EN-336
8.	(S278 FISHWICK CORNER CONSTRUCTION DETAILS SHEET 2)	PA590-EN-337A
9.	(S278 FISHWICK CORNER CONSTRUCTION DETAILS SHEET 3)	PA590-EN-338A
10.	(S278 SOUTHERN ACCESS GA)	PA590-EN-340
11.	(S278 FISHWICK CORNER WATERCOURSE CONSENT)	PA590-EN-339A
12.	(S278 SOUTHERN ACCESS AND MOUNT ROAD CONSTRUCTION DETAILS SHEET 1)	PA590-EN-342
13.	(S278 MOUNT ROAD GA)	PA590-EN-341
14.	(S278 SOUTHERN ACCESS AND MOUNT ROAD CONSTRUCTION DETAILS SHEET 2)	PA590-EN-343
15.	Thurston Beyton Rd Barton Rd & Fishwick Cnr S278 Wrks - Approved Street Lighting 20th November 2023 SHEET 5	
16.	Thurston Beyton Rd Barton Rd & Fishwick Cnr S278 Wrks - Approved Street Lighting 20th November 2023 SHEET 2	



GENERAL
1. DO NOT SCALE THIS DRAWING. ALL DIMENSIONS ARE IN METRES
UNLESS OTHERWISE NOTED. ANY DISCREPANCIES ARE TO BE
RECORDED AND REPORTED TO THE ENGINEERS IMMEDIATELY.

S278 SITE LOCATION KEY

DEVELOPERS OWNERSHIP
BOUNDARY

Rev	Revision Notes	Drawn	Approved	Date
A	MASTERPLAN UPD			



INGENT
CONSULTING ENGINEERS

Unit 1a Greenwood Court, Skyliner Way, Bury St Edmunds, IP32 7GY.
Tel: 01284 245024 ---- www.ingent.co.uk ---- email: info@ingent.co.uk

PRELIMINARY

Project
BEYTON ROAD, THURSTON
SUFFOLK


Drawing Title
S278 WORKS
LOCATION PLAN


Client BLOOR HOMES	Date JUL 2020
-----------------------	------------------

Drawn by KLK	Designed by KLK	Checked by KK	Approved by KK
-----------------	--------------------	------------------	-------------------

Scale
1:2500
50m 0m 50m 100m 150m

Drawing No. PA590-EN-001	Revision. A	Size A3
-----------------------------	----------------	------------

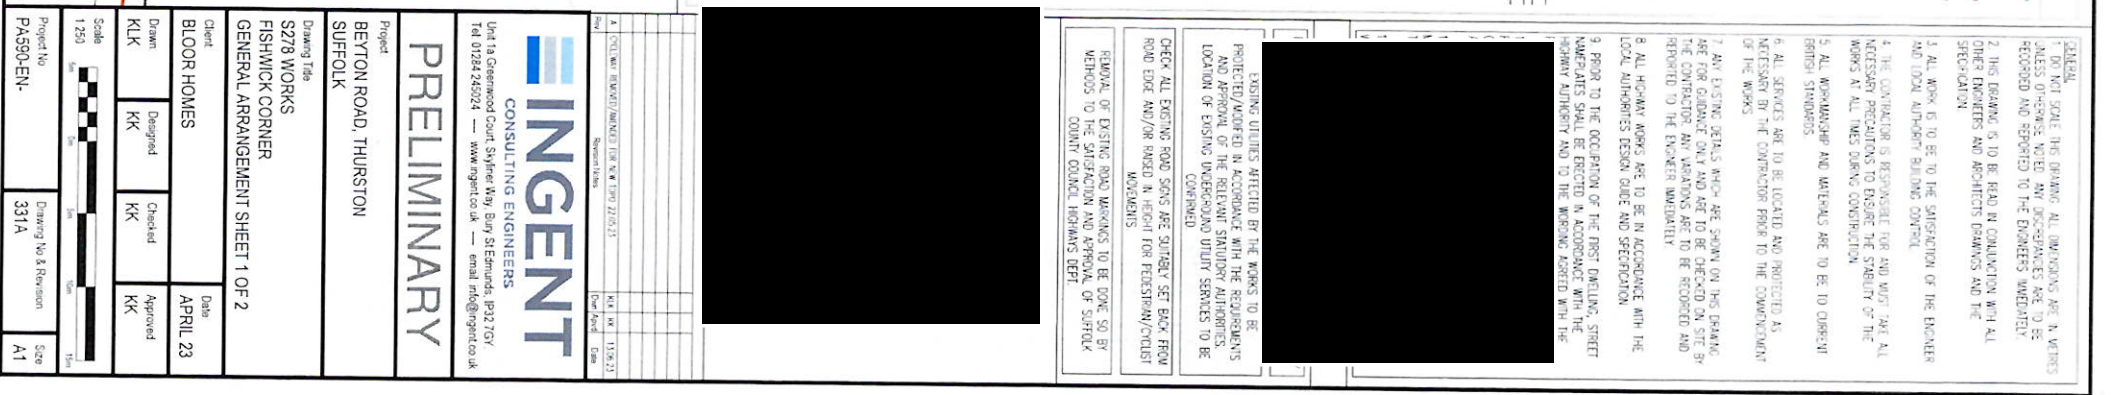

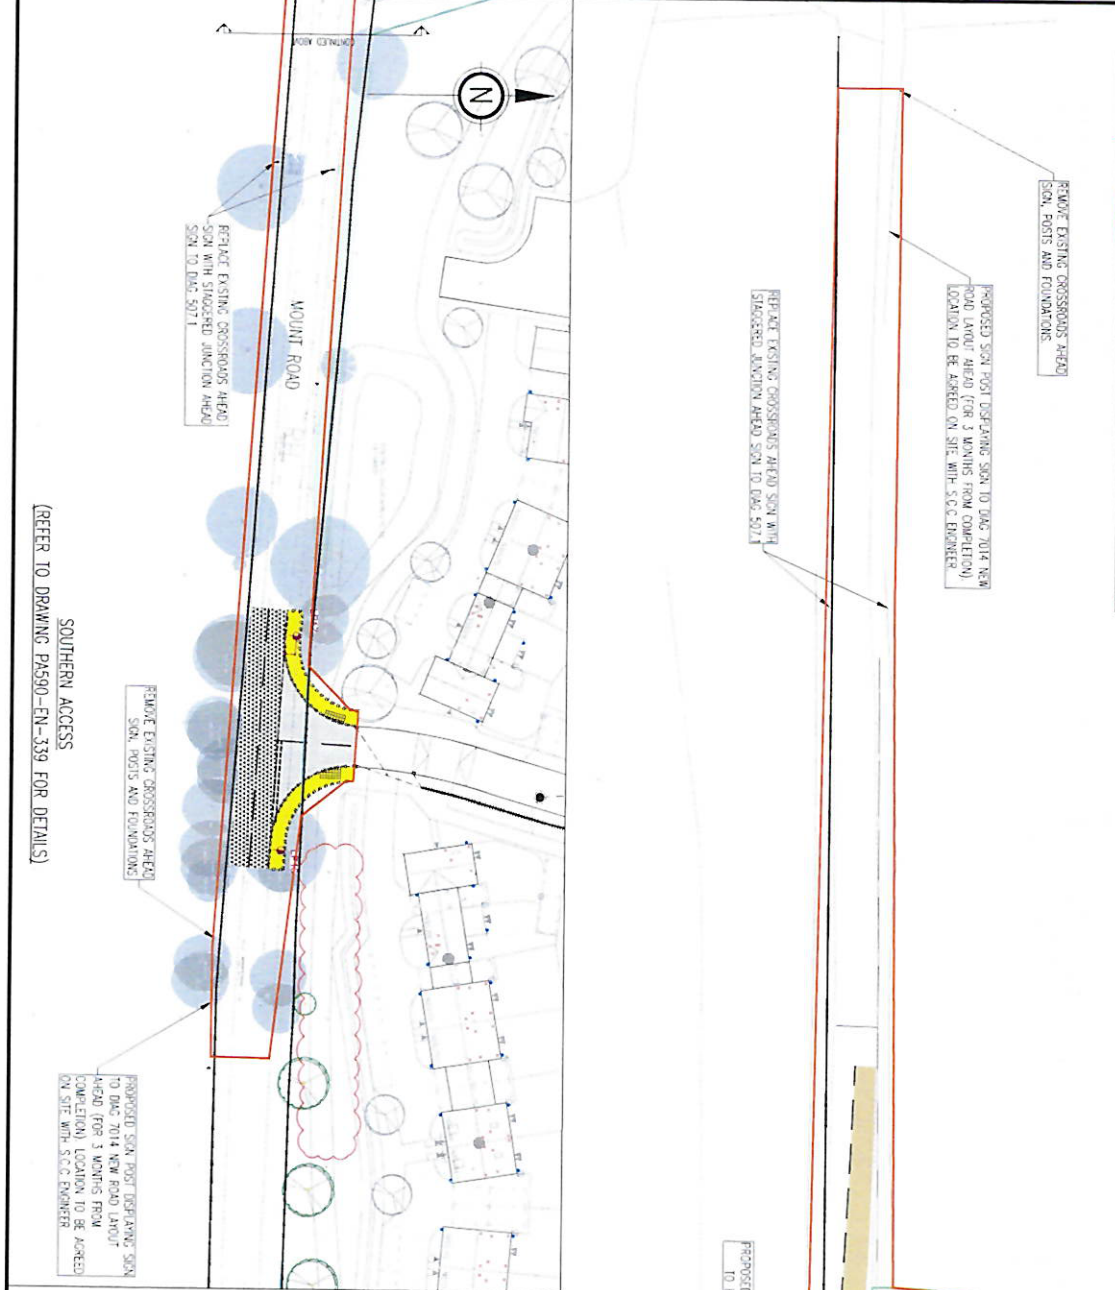

PROPOSED NEW EXTERNALLY ILLUMINATED SIGN TO D46, 602 ONE WAY, 9000mm HEIGHT ON NEW POST IN VERGE - 1.5m MOUNTING HEIGHT, 1200mm KERB OFFSET TO SIGN EDGE.
NEW SIGN TO D46, 531A, AVAILABLE HEADROOM AT ARCH BRIDGE APPROX. SIGN TO BE MOUNTED ON REVERSE EXACT SIGN POSITION AND FACE ANGLE TO TRAFFIC, TO BE AGREED ON SITE BY THE S.C.C. ENGINEER.

EXISTING FINDER POST SIGN PLATE
(TO BARTON ROAD) TO BE REMOVED

PROPOSED SIGN POST DISPLAYING SIGN TO DMC 2014 NEW
ROAD LAYOUT AHEAD (FOR 3 MONTHS FROM COMPLETION)
LOCATION TO BE AGREED ON SITE WITH S.C.C. ENGINEER






SOUTHERN ACCESS
(REFER TO DRAWING PA590-EN-339 FOR DETAILS)

Ingent Consulting Engineers LTD. Head office/Registered office Unit 10 Brightwell Barns, Watlingfield Road, Suffolk, IP10 0BJ. Tel 01473 598038. Registered No 912048.

1. DO NOT SCALE THE DRAWING. ALL DIMENSIONS ARE IN METERS UNLESS OTHERWISE NOTED AND DIMENSIONS ARE TO BE RECORDED AND REPORTED TO THE ENGINEERS IMMEDIATELY.
2. THE DRAWING IS TO BE READ A CONTRACTOR WITH ALL LOCAL CONDITIONS AND PROJECTS DRAWINGS AND THE SPECIFICATION.
3. ALL WORK IS TO BE TO THE SATISFACTION OF THE OWNER AND LOCAL AUTHORITY ENGINEERING CONTROL.
4. THE CONTRACTOR IS RESPONSIBLE FOR AND MUST HAVE ALL NECESSARY PERMITS TO ENSURE THE STABILITY OF THE WORKS AT ALL TIMES DURING CONSTRUCTION.
5. ALL WORKMANSHIP AND MATERIALS ARE TO BE TO CORRECT BRITISH STANDARDS.
6. ALL SERVICES ARE TO BE LOCATED AND PROTECTED AS NECESSARY BY THE CONTRACTOR PRIOR TO THE CONSTRUCTION OF THE WORKS.
7. ALL EXISTING DETAILS WHICH ARE SHOWN ON THIS DRAWING ARE FOR INFORMATION ONLY AND ARE TO BE CHECKED ON SITE BY THE CONTRACTOR. ANY ASSUMED DETAILS ARE TO BE RECORDED AND REPORTED TO THE ENGINEER IMMEDIATELY.
8. ALL HIGHWAY WORKS ARE TO BE IN ACCORDANCE WITH THE LOCAL AUTHORITY DESIGN GUIDE AND SPECIFICATION.
9. PRIOR TO THE OCCUPATION OF THE FIRST BUILDING, STREET LIGHTS SHALL BE INSTALLED IN ACCORDANCE WITH THE RELEVANT AUTHORITY AND TO THE WORKING AGREED WITH THE RELEVANT AUTHORITY.
10. TO DRAIN CONSTRUCTION WORKS ON SITE, ALL PIPES AND ROPEWAYS ARE TO BE SHUT OFF AND KEPT CLEAR OF OBSTRUCTIONS. THIS IS TO INCLUDE EXISTING HIGHWAYS AS APPROPRIATE, TO ENSURE SAFE PASSAGE OF ALL ROAD USERS.
11. PROVISION SHALL BE MADE FOR THE INSTALLATION OF ALL MAINS SERVICES INCLUDING DUCTING PRIOR TO THE LAYING OF THE ROAD BED COURSE.
12. ALL ROAD WORKS AND WORKS ARE TO BE IN ACCORDANCE WITH THE RELEVANT STANDARDS REGULATIONS AND DIRECTIONS 2016.

CHECK ALL EXISTING ROAD SIGNS ARE SURELY SET BACK FROM ROAD EDGE AND/OR BASED IN RIGHT-OF-WAY FOR PEDESTRIAN/CYCLIST MOVEMENTS

Circumstance	Percentage of Respondents (%)
If someone is attacking you	85
If someone is threatening you	75
If someone is harassing you	65
If someone is insulting you	55
If someone is annoying you	45

<p>PLANE AND INLAY SURFACE COURSE 60 PLY TO REFACE EXISTING HFS</p>	
<p>5278 PROPOSED LIGHT COLUMN OFFSET TO LIGHTING DRAWINGS SL/0007/001 SHEET 1-5)</p>	
<p>5278 PROPOSED ILLUMINATED TRAFFIC SIGNS (REFER TO STREET LIGHTING DRAWINGS SL/0007/001 SHEET 1-5)</p>	
<p>5278 PROPOSED TIMBER POST AND RAIL FENCE</p>	
<p>PROPOSED NATIVE HEDGE</p>	


A	Title	GENERAL ARRANGEMENT SHEET 2 OF 2	Project No.	3324	Drawing No.	3324	Revision	A
B	Client	BLOOR HOMES	Drawing Title	S2/8 WORKS	FISHWICK CORNER	GENERAL ARRANGEMENT SHEET 2 OF 2	Date	APRIL 22
C	Project	BAYTON ROAD, THURSTON	Project No.	3324	Drawing No.	3324	Revision	A
D	Consulting Engineer	INGENT CONSULTING ENGINEERS	Project No.	3324	Drawing No.	3324	Revision	A
E	Project	BAYTON ROAD, THURSTON	Project No.	3324	Drawing No.	3324	Revision	A
F	Project	BAYTON ROAD, THURSTON	Project No.	3324	Drawing No.	3324	Revision	A
G	Project	BAYTON ROAD, THURSTON	Project No.	3324	Drawing No.	3324	Revision	A
H	Project	BAYTON ROAD, THURSTON	Project No.	3324	Drawing No.	3324	Revision	A
I	Project	BAYTON ROAD, THURSTON	Project No.	3324	Drawing No.	3324	Revision	A
J	Project	BAYTON ROAD, THURSTON	Project No.	3324	Drawing No.	3324	Revision	A
K	Project	BAYTON ROAD, THURSTON	Project No.	3324	Drawing No.	3324	Revision	A
L	Project	BAYTON ROAD, THURSTON	Project No.	3324	Drawing No.	3324	Revision	A
M	Project	BAYTON ROAD, THURSTON	Project No.	3324	Drawing No.	3324	Revision	A
N	Project	BAYTON ROAD, THURSTON	Project No.	3324	Drawing No.	3324	Revision	A
O	Project	BAYTON ROAD, THURSTON	Project No.	3324	Drawing No.	3324	Revision	A
P	Project	BAYTON ROAD, THURSTON	Project No.	3324	Drawing No.	3324	Revision	A



New Road				
Chainage (m)	Easting (m)	Northing (m)	Level (m)	Curve/Straight
0.000	591718.954	264745.459	45.201	Start
0.001	591718.954	264745.458	45.201	IP at Channel
0.047	591718.946	264745.413	45.200	Tangent Point
10.000	591716.807	264736.695	45.121	Curve Radius 132.784
20.000	591713.931	264726.119	45.073	Curve
30.000	591710.343	264716.788	45.109	Curve
40.000	591706.063	264707.753	45.189	Curve
50.000	591699.115	264699.085	45.265	Curve
60.000	591689.528	264690.775	45.345	Curve
70.000	591682.332	264682.920	45.425	Curve
80.000	591678.855	264675.570	45.505	Curve
85.168	591678.019	264671.972	45.547	Curve
86.310	591678.019	264671.972	45.547	Tangent Point
90.000	591673.564	264668.592	45.586	Curve Radius 38.784
92.967	591673.564	264668.592	45.586	Tangent Point
94.711	591672.910	264664.888	45.609	Tangent Point
100.000	591669.498	264660.531	45.623	Curve Radius 66.721
109.357	591664.431	264652.235	45.665	Tangent Point
110.000	591664.431	264651.738	45.665	Straight
111.116	591663.953	264650.180	45.759	Tangent Point
112.831	591663.702	264649.792	45.767	Curve Radius 7.025
112.840	591663.702	264649.792	45.767	Tangent Point
120.000	591661.935	264642.173	45.825	Tangent Point
129.091	591661.190	264637.137	45.866	Curve Radius 64.901
127.796	591660.900	264634.448	45.888	Tangent Point
127.797	591660.900	264634.447	45.888	IP at Channel
127.797	591660.900	264634.447	45.888	End

Road 1				
Chainage (m)	Easting (m)	Northing (m)	Level (m)	Curve/Straight
0.000	591725.148	264702.114	45.390	Start
10.000	591715.725	264703.353	45.235	Straight
17.997	591707.359	264704.934	45.185	IP at Channel
20.000	591705.538	264703.825	45.185	Straight
20.677	591704.943	264703.548	45.204	End

Road 1T				
Chainage (m)	Easting (m)	Northing (m)	Level (m)	Curve/Straight
0.000	591709.510	264690.770	45.224	Start
10.000	591711.185	264700.529	45.125	Straight
10.453	591711.281	264701.076	45.121	IP at Channel
13.203	591711.602	264703.805	45.189	End

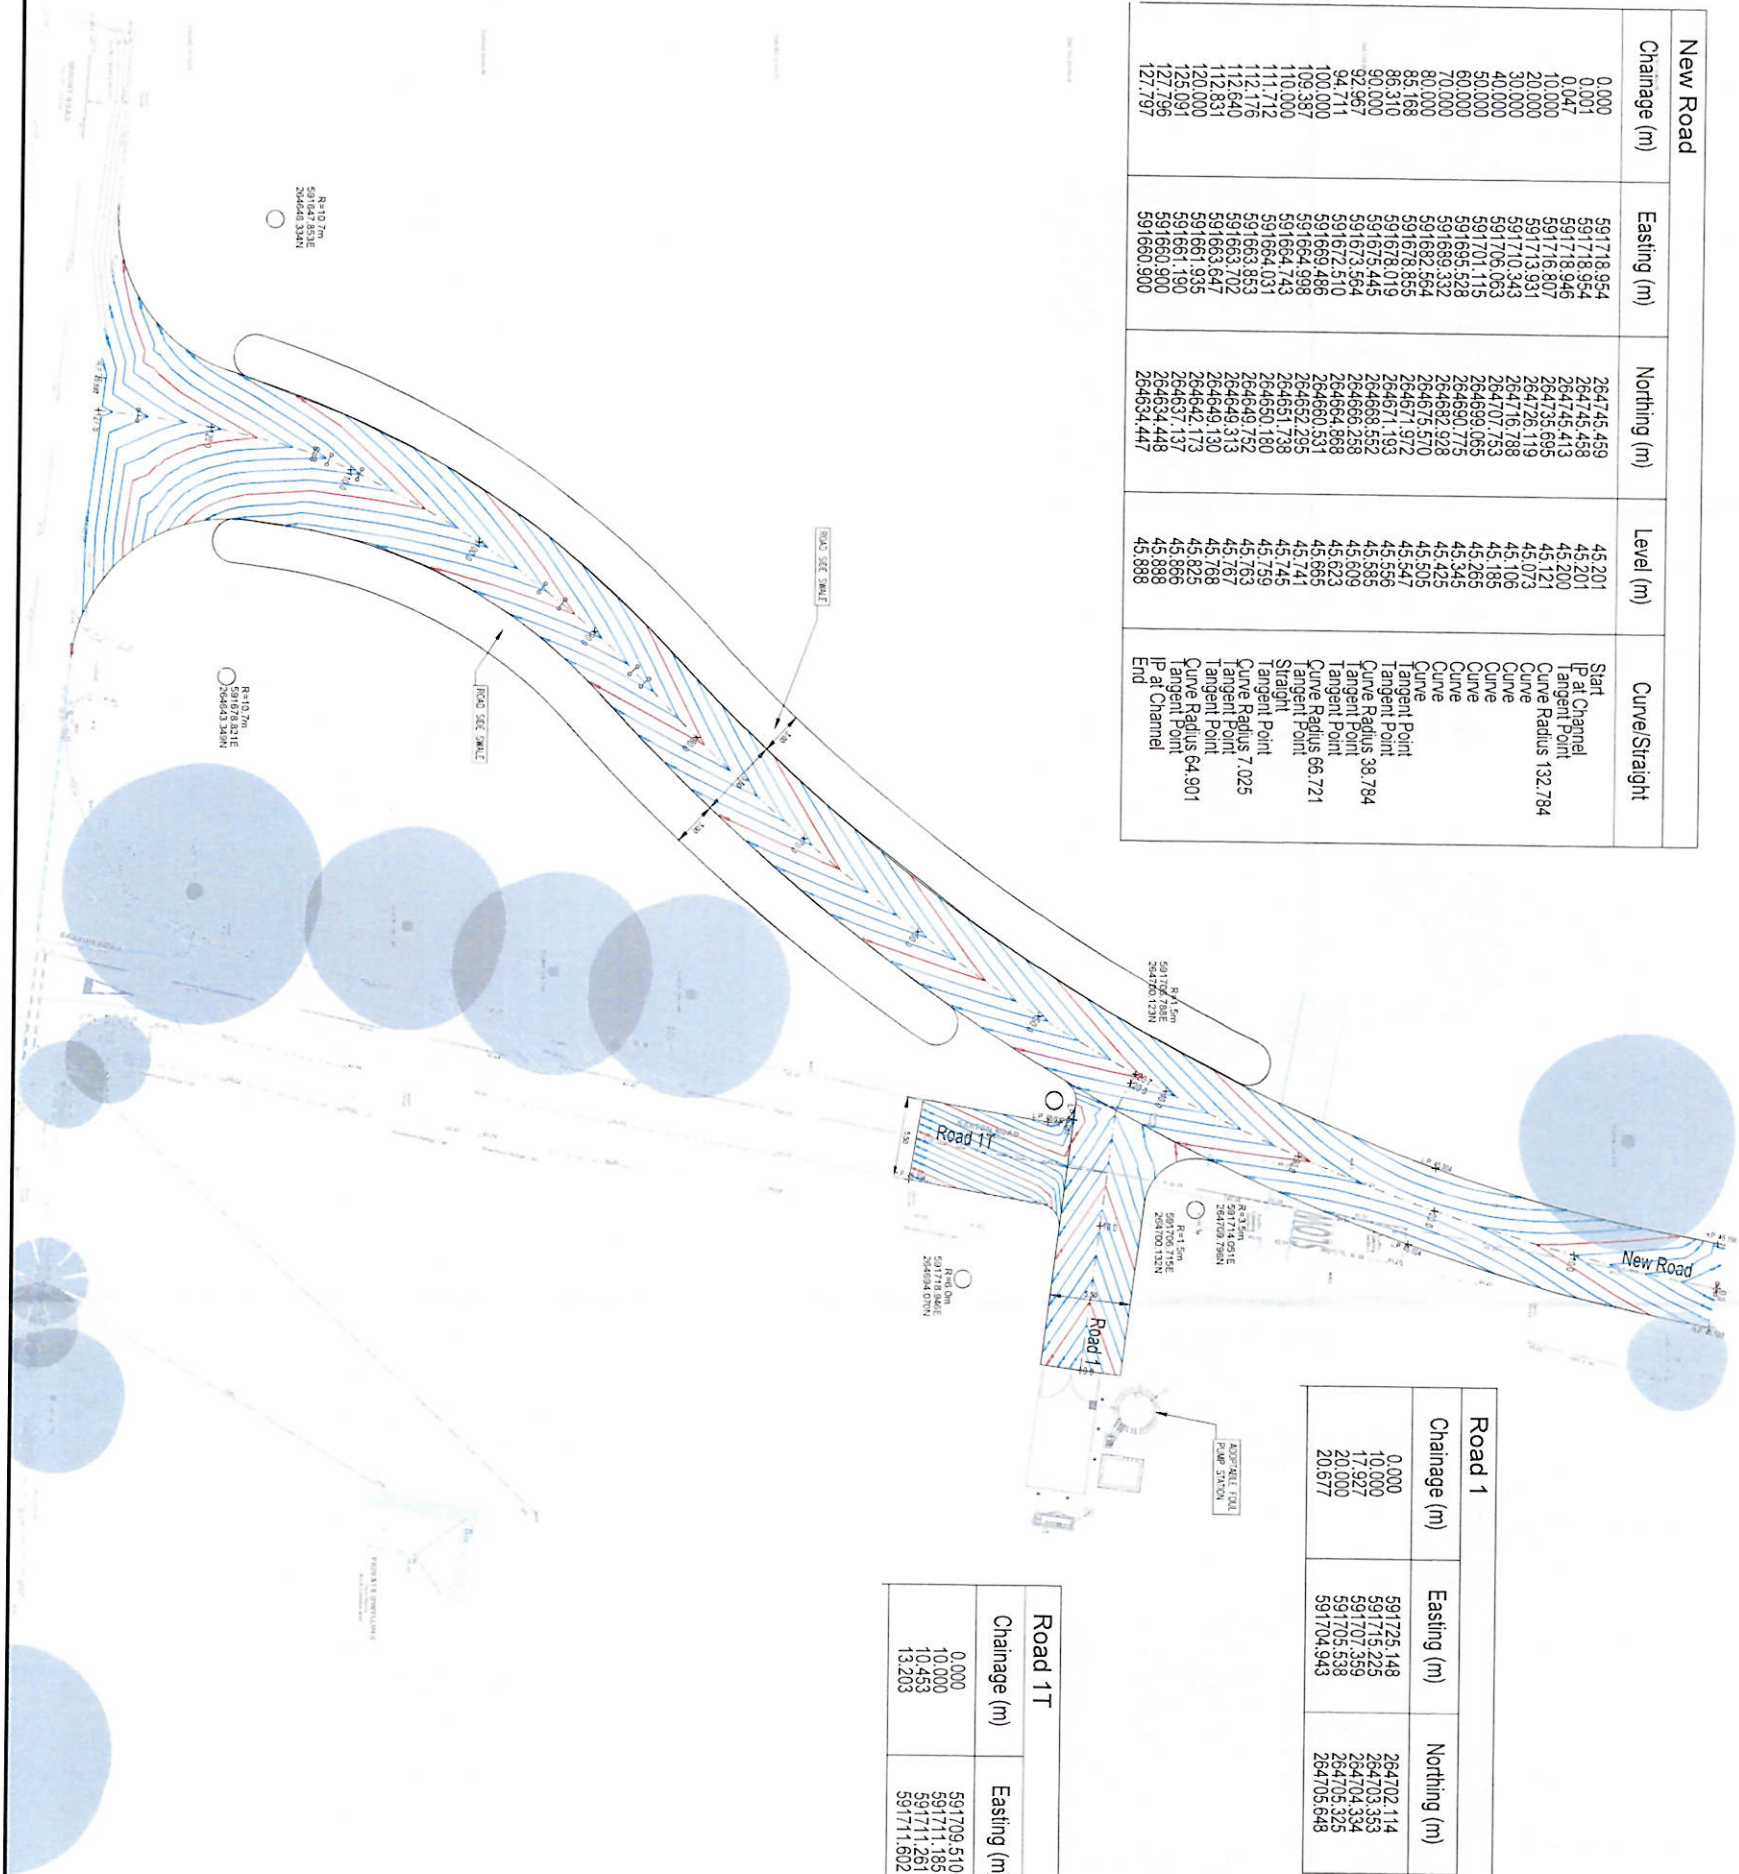

NOTES

1. FOR NOT SCALE THIS DRAWING. ALL DIMENSIONS ARE IN METERS.
2. ALL DIMENSIONS, NOTES AND DISCREPANCIES ARE TO BE RECORDED AND REPORTED TO THE ENGINEERS IMMEDIATELY.
3. THIS DRAWING IS TO BE READ IN CONJUNCTION WITH ALL OTHER DRAWINGS AND RELEVANT STANDARDS AND THE SPECIFICATION.
4. ALL WORK IS TO BE TO THE SATISFACTION OF THE ENGINEER AND LOCAL AUTHORITY BUILDING CONTROL.
5. THE CONTRACTOR IS RESPONSIBLE FOR AND MUST TAKE ALL NECESSARY PRECAUTIONS TO ENSURE THE SAFETY OF THE WORKERS AT ALL TIMES DURING CONSTRUCTION.
6. ALL MATERIALS AND MATERIALS ARE TO BE TO CURRENT BRITISH STANDARDS.
7. ALL SERVICES ARE TO BE LOCATED AND PROTECTED AS NECESSARY BY THE CONTRACTOR PRIOR TO THE COMMENCEMENT OF THE WORKS.
8. ANY EXISTING UTILITIES WHICH ARE SHOWN ON THIS DRAWING ARE TO BE PROTECTED AND NOT TO BE DAMAGED OR REMOVED. ANY UTILITIES ARE TO BE RECORDED AND REPORTED TO THE ENGINEER IMMEDIATELY.
9. ALL HIGHWAY WORKS ARE TO BE IN ACCORDANCE WITH THE LOCAL AUTHORITY'S DESIGN CODE AND SPECIFICATION.
10. PRIOR TO THE OCCUPATION OF THE FIRST DETAILING, STREET LIGHTS SHALL BE ERECTED IN ACCORDANCE WITH THE PLANNING AUTHORITY AND TO THE WORKING AGREED WITH THE PLANNING AUTHORITY.
11. DURING CONSTRUCTION WORKS ON SITE, ALL BORDERS AND FENCINGS ARE TO BE SURET AND KEPT CLEAR OF OBSTRUCTIONS. THIS IS TO INCLUDE EXISTING HIGHWAYS AS APPROPRIATE TO ENSURE SAFE PASSAGE OF ALL ROAD USERS.
12. PROVISION SHALL BE MADE FOR THE INSTALLATION OF ALL WORKS SERVICES INCLUDING DUCTING PRIOR TO THE LAYING OF THE ROAD DECK CONCRETE.
13. ALL ROAD WORKS AND SIGNS ARE TO BE IN ACCORDANCE WITH THE LATEST SIGN REGULATIONS AND DIRECTIONS 2016.

INGENT
CONSULTING ENGINEERS

Unit 1a Greenwood Court, Station Way, Bury St Edmunds, IP12 7DT.
Tel: 01284 246974 — www.ingent.co.uk — email: info@ingent.co.uk

PRELIMINARY

Project: BEYTON ROAD, THURSTON
SUFFOLK

Drawing Title: S278 WORKS
ROAD SETTING OUT
FISHWICK CORNER



Client:	BLOOR HOMES	Date:	APRIL 23
Drawn:	KLK	Checked:	RGW
KLK	RGW	Approved:	RGW


Scale: 1:250

Project No: PA590-EN-1

Drawing No & Revision: 333A

Size: A1

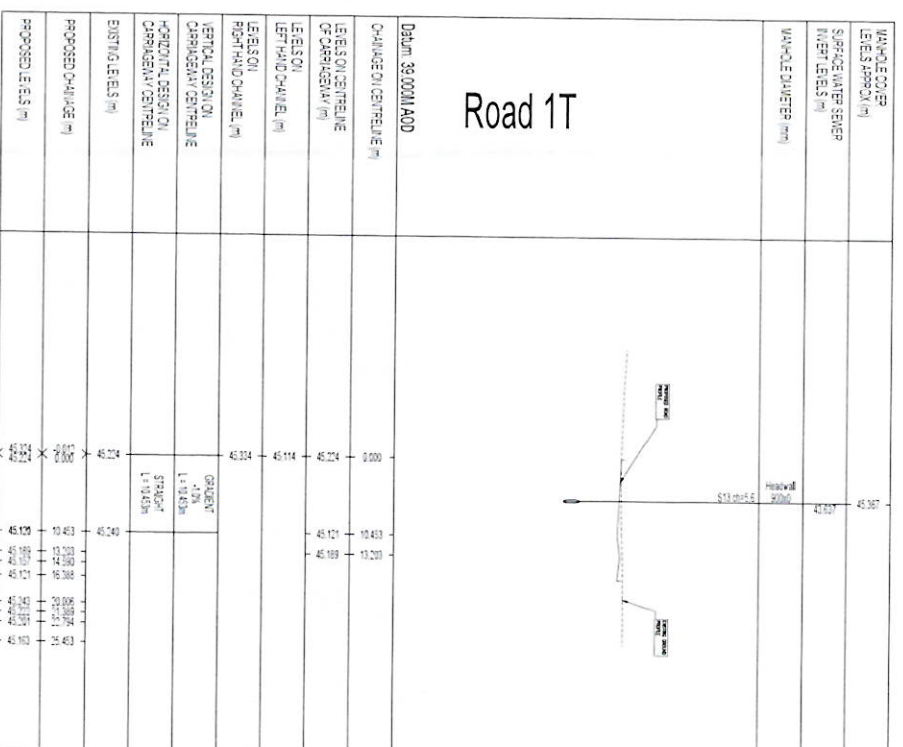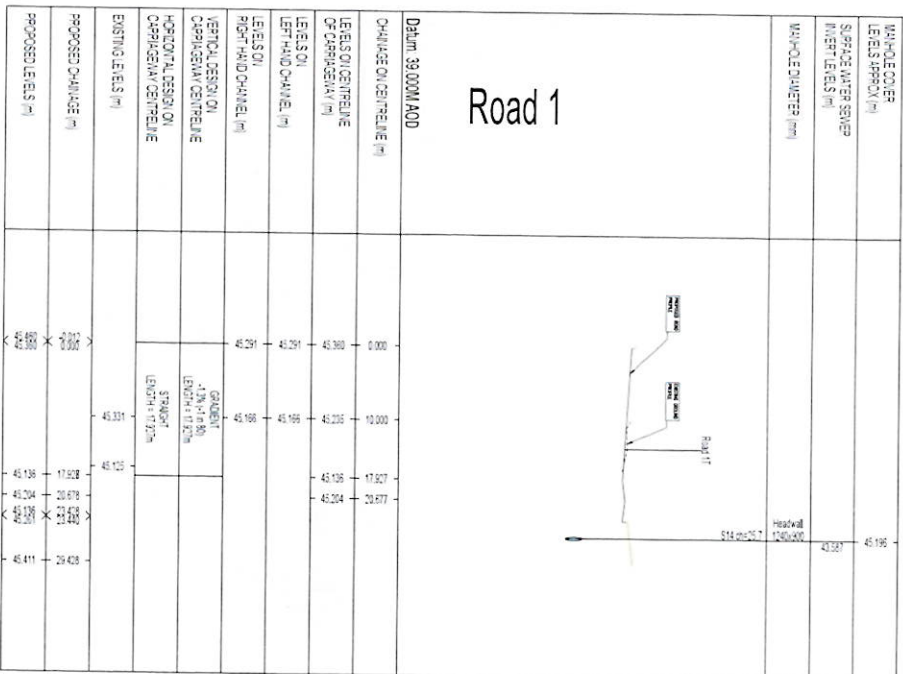



CONSULTING ENGINEERS
Unit 1a Greenwood Court, Skyliner Way, Bury St Edmunds, IP32 7GY
Tel 01284 245024 — www.ingent.co.uk — email info@ingent.co.uk

PRELIMINARY

Project
BEYTON ROAD, THURSTON
SUFFOLK

Drawing Title
S278 WORKS FISHWICK CORNER
& SOUTHERN ACCESS
LAND DEDICATION PLAN


BLOOR HOMES		APRIL 2023
Drawn KLK	Designed KLK	Checked KK
		Approved KK





Project No	Drawing No & Revision	Size
PA590-EN-	335A	A1




SCALE 1:10

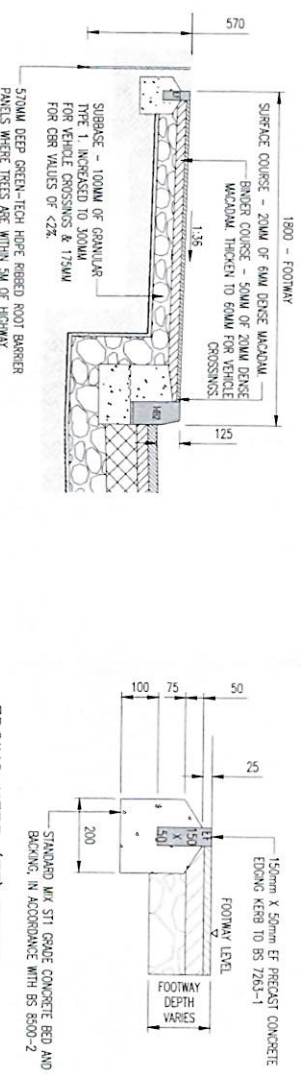







SCALE 1:20

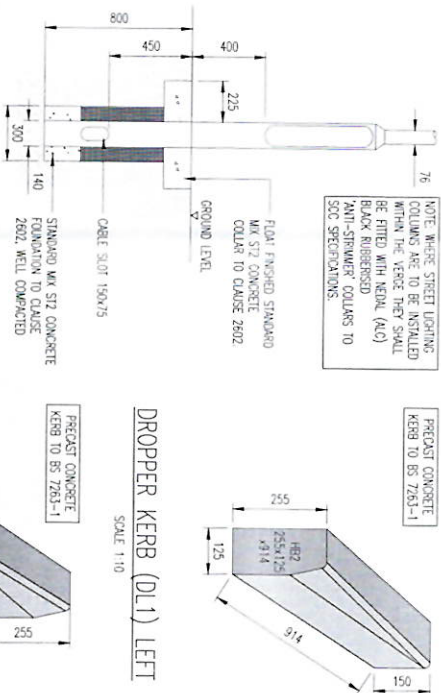

SCALE 1:10



SCALE 1:

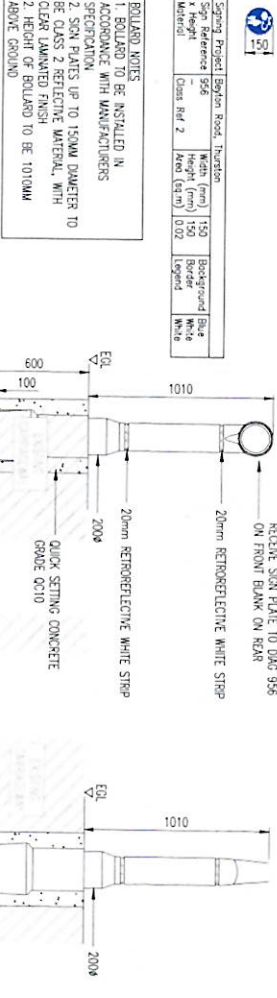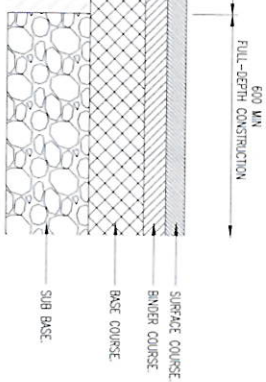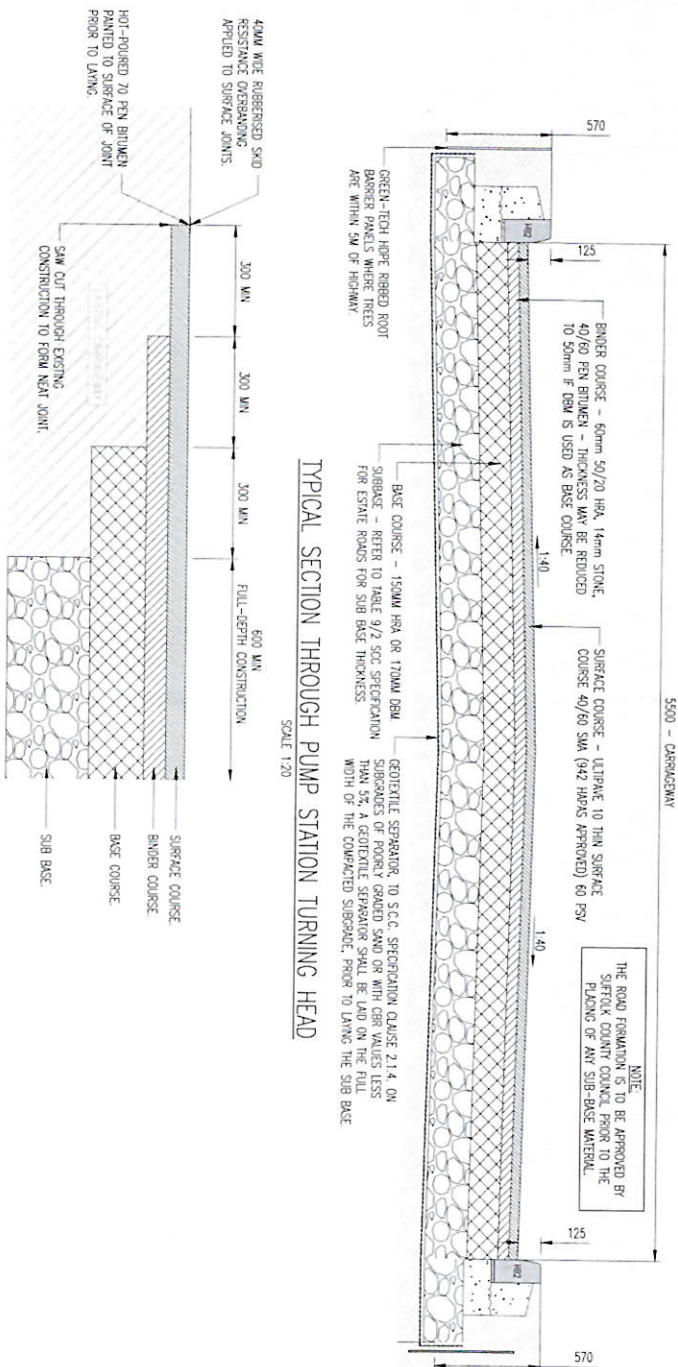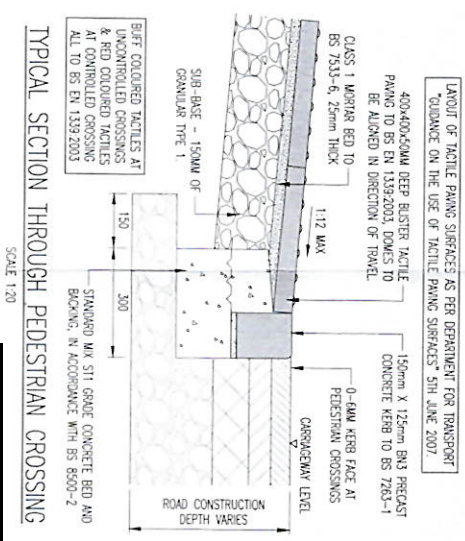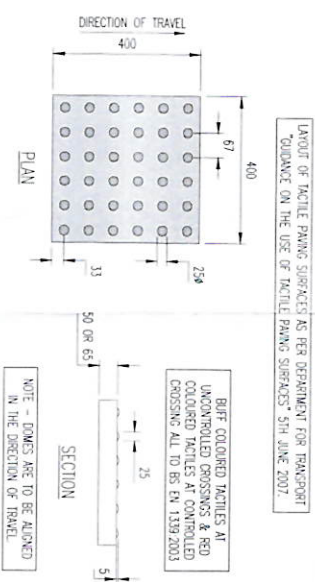

20mm RETROREFLECTIVE WHITE STRIP

2000

600

100

1000

QUICK SETTING CONCRETE

GRADE 0+10

BOLLARD MARKERS

1. BOLLARD TO BE INSTALLED IN ACCORDANCE WITH MANUFACTURERS SPECIFICATIONS
2. SIGN SHALL BE 150MM DIA. TO 150MM DIA. TO BE CLASS 2 REFLECTIVE MATERIAL, WITH CLEAR LAMINATED FINISH
3. HEIGHT OF BOLLARD TO BE 1010MM ABOVE GROUND




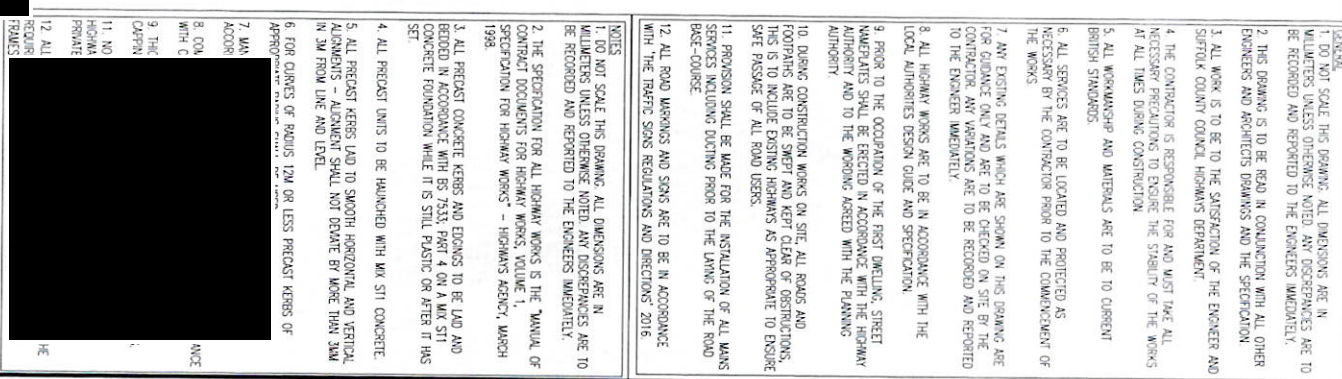


TABLE 7.1


PIPE DIAMETER (mm)	STONE SIZED AGGREGATE (mm) TO BS 882
LESS THAN 150mm	10
INCLUDING 150mm UP TO 200mm	10 OR 14
INCLUDING 200mm UP TO 250mm	14 OR 20
INCLUDING 250mm AND ABOVE	14, 20 OR 40

NOTES:
1. 200mm THICK FLEXIBLE OR STABLE APPROVED FILTER TO BE USED TO PROTECT FROM A FLEXIBLE JOINT TO THE CONCRETE SUBGRADE AT THE LEADING EDGE OF A STABLE COURSE. DIMENSIONS SHOWN ARE REPRESENTATIVE OF TYPE 2. IF A STABLE COURSE IS USED, THE JOINTS ARE TO BE PROTECTED FROM THE LEADING EDGE OF CONCRETE BY A MINIMUM OF 100mm POLYURETHANE SHEET OR BUILDING PAPER.

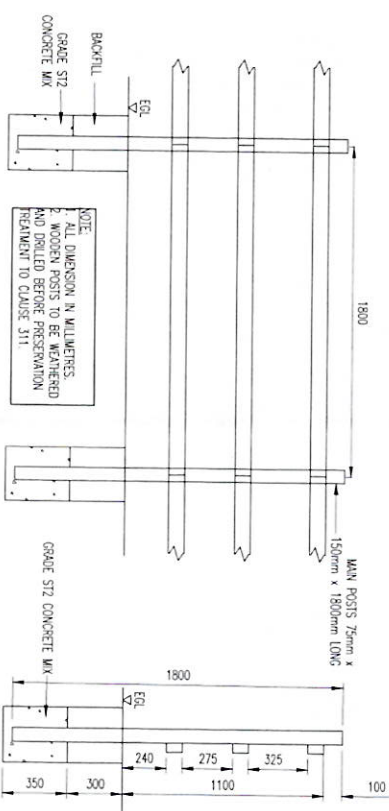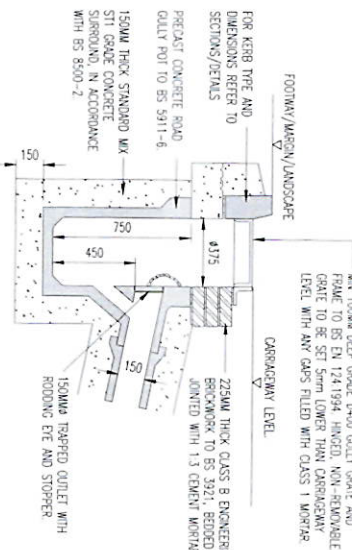


TYPICAL ROAD GULLY DETAIL
SCALE 1:20


- GULLY NOTES:
1. GULLY FRAMING AND FRAME TO BS EN 124 REFER TO SPECIFICATION FOR ROAD CLASSE 7.13.4
2. GULLY FRAME TO BE SET ON 10-20mm THICK CLASS 1 CEMENT MORTAR BED TO CLASS 7.13.4 (UNLESS OTHERWISE SPECIFIED)
3. GULLY FRAME TO BE SET ON 10-20mm THICK CLASS 1 CEMENT MORTAR BED TO CLASS 7.13.4 (UNLESS OTHERWISE SPECIFIED)
4. WHERE THE GULLY CONNECTION PRELIMINARY PRESSURES UNDER THE GULLY SHALL BE SET AT LEAST 175mm BELOW FORMATION LEVEL, THE INSERT SHALL BE AT LEAST 175mm BELOW THE TOP OF THE SUB-AGE.
5. NOTES 3 & 4 WHERE THE TOTAL ROAD CONSTRUCTION DEPTH EXCEEDS 450mm AND THE GULLY CONNECTION PIPE PASSES UNDER THE DRIVEWAY UP TO 5 COURSE OF BROOKWAY ARE REQUIRED.

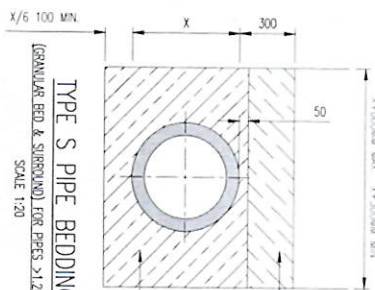


TYPE S PIPE BEDDING
SCALE 1:20

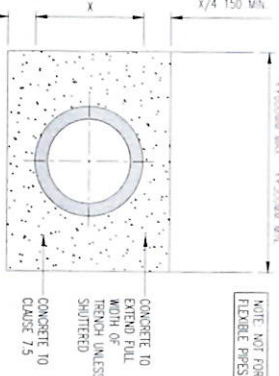


TYPE Z PIPE BEDDING
(CONCRETE SURROUND)
SCALE 1:20



TYPICAL SECTION THROUGH SWALE CHECK DAM
SCALE 1:20

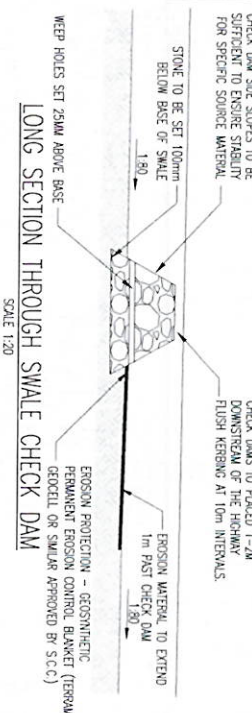


LONG SECTION THROUGH SWALE CHECK DAM
SCALE 1:20

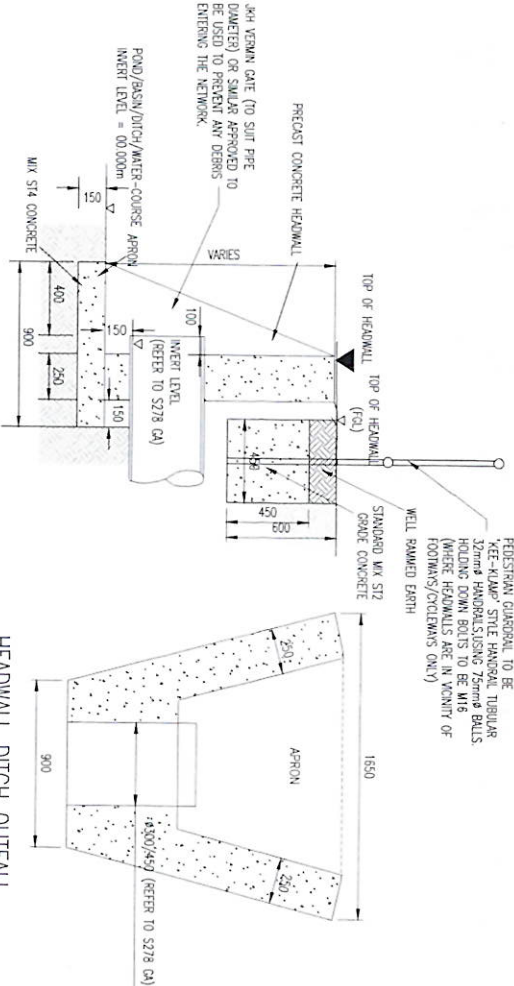


HEADWALL DITCH OUTFALL DETAIL
SCALE 1:20

HEADWALL DITCH OUTFALL
PLAN VIEW
SCALE 1:20

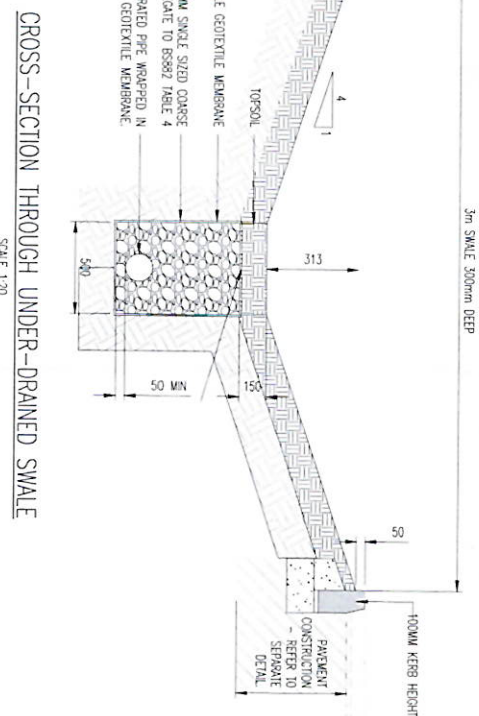

CROSS-SECTION THROUGH UNDER-DRAINED SWALE
SCALE 1:20

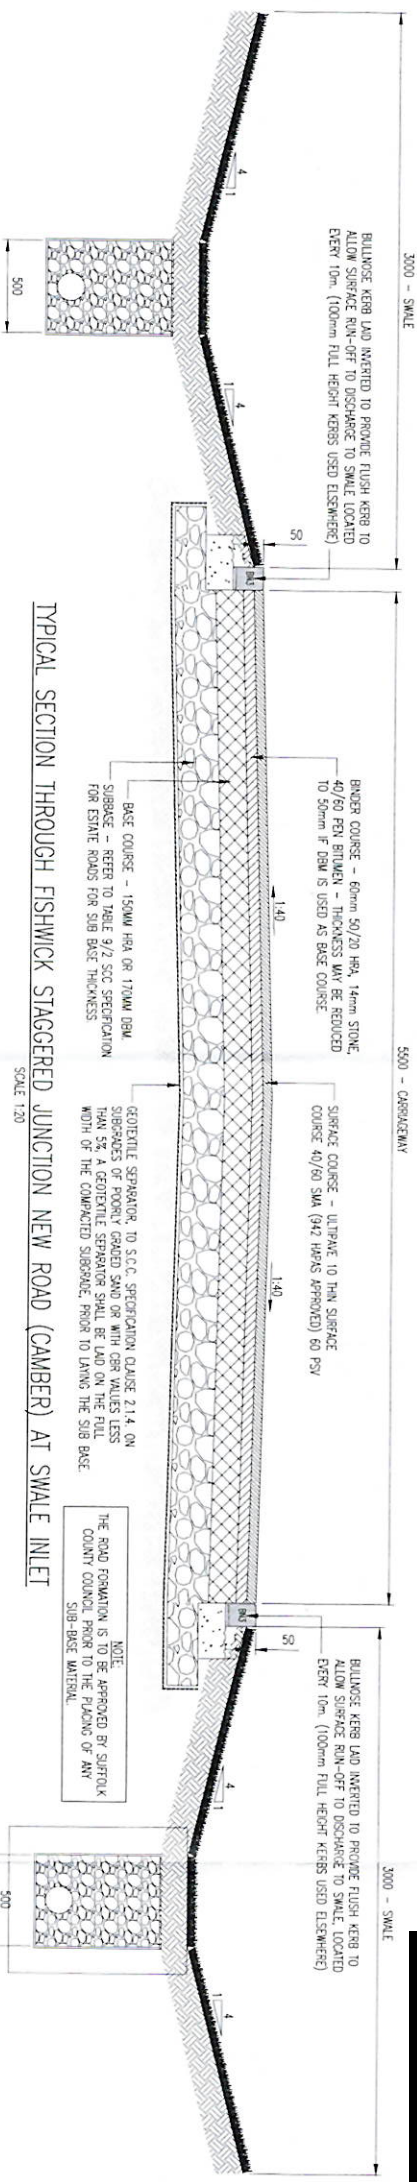

TYPICAL SECTION THROUGH FISHWICK STAGGERED JUNCTION NEW ROAD (CAMBER) AT SWALE INLET
SCALE 1:20




Sign Reference	Sign Type	Sign Size	Sign Material	Sign Colour	Sign Shape	Sign Mounting
1014	Rectangular	750 x 500	Aluminium	White	Rectangular	Post

POST TO BE NOT DIPPED GALVANIZED STEEL

Standard Construction Details	Reference	Quantity	Notes
1. 100mm THICK FLEXIBLE OR STABLE APPROVED FILTER TO BE USED TO PROTECT FROM A FLEXIBLE JOINT TO THE CONCRETE SUBGRADE AT THE LEADING EDGE OF A STABLE COURSE. DIMENSIONS SHOWN ARE REPRESENTATIVE OF TYPE 2. IF A STABLE COURSE IS USED, THE JOINTS ARE TO BE PROTECTED FROM THE LEADING EDGE OF CONCRETE BY A MINIMUM OF 100mm POLYURETHANE SHEET OR BUILDING PAPER.	1014	1	

TEMPORARY SIGN POSITIONED IN VERGE FOR 3 MONTHS FROM COMPLETION SIGN AND POST DETAILS
SCALE 1:20

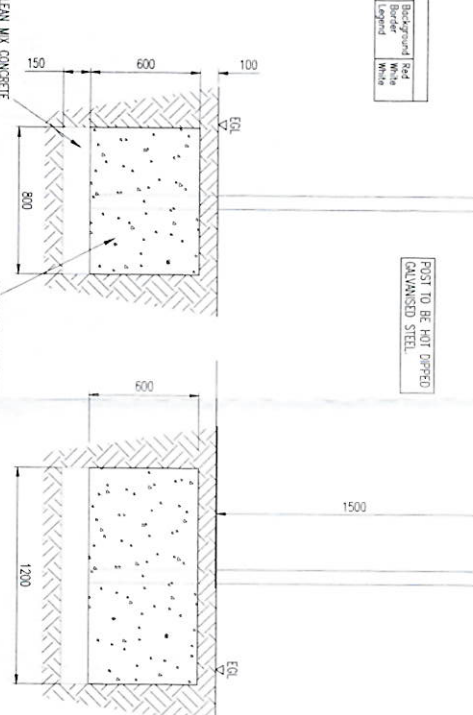

DETAIL AT 25MM UPSTAND
SCALE 1:20

DETAIL AT FLUSH KERB
SCALE 1:20




- GENERAL:
1. DO NOT SCALE THIS DRAWING. ALL DIMENSIONS ARE IN MILLIMETERS UNLESS OTHERWISE NOTED. ANY DISCREPANCIES ARE TO BE RECORDED AND REPORTED TO THE ENGINEER IMMEDIATELY.
2. THIS DRAWING IS TO BE READ IN CONJUNCTION WITH ALL OTHER DRAWINGS AND ARCHITECT'S DRAWINGS AND THE SPECIFICATION.
3. ALL WORK IS TO BE TO THE SATISFACTION OF THE ENGINEER AND SUFFOLK COUNTY COUNCIL HIGHWAYS DEPARTMENT.
4. THE CONTRACTOR IS RESPONSIBLE FOR AND MUST TAKE ALL NECESSARY PRECAUTIONS TO ENSURE THE STABILITY OF THE WORKS AT ALL TIMES DURING CONSTRUCTION.
5. ALL WORKSHOPS AND MATERIALS ARE TO BE TO CURRENT BRITISH STANDARDS.
6. ALL SERVICES ARE TO BE LOCATED AND PROTECTED AS NECESSARY BY THE CONTRACTOR PRIOR TO THE COMMENCEMENT OF THE WORKS.
7. ANY EXISTING DETAILS WHICH ARE SHOWN ON THIS DRAWING ARE FOR GUIDANCE ONLY AND ARE TO BE CHECKED ON SITE BY THE CONTRACTOR. ANY VARIATIONS ARE TO BE RECORDED AND REPORTED TO THE ENGINEER IMMEDIATELY.
8. ALL HIGHWAY WORKS ARE TO BE IN ACCORDANCE WITH THE LOCAL AUTHORITIES DESIGN GUIDE AND SPECIFICATION.
9. PRIOR TO THE OCCUPATION OF THE FIRST COMPLETING STREET, THE CONTRACTOR SHALL BE RESPONSIBLE FOR THE PROTECTION OF THE HIGHWAY AUTHORITY AND TO THE WORKING AGREED WITH THE PLANNING AUTHORITY.
10. DURING CONSTRUCTION WORKS ON SITE ALL ROADS AND FOOTPATHS TO BE SHUT AND KEPT CLEAR OF OBSTRUCTIONS. THE CONTRACTOR SHALL BE RESPONSIBLE FOR THE PROTECTION OF THE HIGHWAY AUTHORITY AND TO THE WORKING AGREED WITH THE PLANNING AUTHORITY.
11. PROVISION SHALL BE MADE FOR THE INSTALLATION OF ALL WORKS SERVICES INCLUDING DUCTING PRIOR TO THE LAYING OF THE ROAD BASE COURSE.
12. ALL ROAD WORKS AND SIGNS ARE TO BE IN ACCORDANCE WITH THE TRAFFIC SIGNS REGULATIONS AND DIRECTIONS 2016.

- NOTES:
1. ARE TO 2.1% FALL OR MORE.
2. ARE TO 2.1% FALL OR MORE.
3. ARE TO 2.1% FALL OR MORE.
4. ARE TO 2.1% FALL OR MORE.
5. ARE TO 2.1% FALL OR MORE.
6. ARE TO 2.1% FALL OR MORE.
7. ARE TO 2.1% FALL OR MORE.
8. ARE TO 2.1% FALL OR MORE.
9. ARE TO 2.1% FALL OR MORE.
10. ARE TO 2.1% FALL OR MORE.
11. ARE TO 2.1% FALL OR MORE.
12. ARE TO 2.1% FALL OR MORE.

INGENT
CONSULTING ENGINEERS
15 Greenwood Court, Station Road, Bury St Edmunds, IP32 7TY
Tel: 01784 245024 — www.ingent.co.uk — email: info@ingent.co.uk

PRELIMINARY	
Project:	BEYTON ROAD, THURSTON SUFFOLK
Client:	S278 WORKS FISHWICK CORNER STANDARD CONSTRUCTION DETAILS SHEET 02 OF 03
Drawn:	KLK
Checked:	KK
Approved:	KK
Date:	APRIL 2023
Scale:	As Shown
Project No:	PA590-EN-
Drawing No & Revision:	337A
Size:	A1



Sign Reference	Width (mm)	Height (mm)	Background	Border	Legend
507.1	750	400	Yellow	Black	Black

Structural Calculation Details

Sign: Reference Sign 1
Width: 750mm, Height: 400mm
Shape: Rectangular
Orientation: Facing front
Mounted on post: 1
Mounting height: 1500mm, at post
Post: 1
Type: 76.1 x 32 CHS
Spacing: N/A
Post 1 Length: 3025mm
Base: Type: Combined
Width: 800mm
Length: 1200mm
Depth: 600mm
Volume: 0.864m³
Earth cover: 100mm
Binding layer: 150mm

DIAG 507.1 STAGGERED CROSSING SIGN AND POST DETAILS
SCALE 1:20

Sign Reference	Width (mm)	Height (mm)	Background	Border	Legend
507.1	750	400	Yellow	Black	Black

Sign Reference	Width (mm)	Height (mm)	Background	Border	Legend
507.1	750	400	Yellow	Black	Black

Structural Calculation Details

Sign: Reference Sign 1
Width: 750mm, Height: 400mm
Shape: Rectangular
Orientation: Facing front
Mounted on post: 1
Mounting height: 1500mm, at post
Post: 1
Type: 76.1 x 32 CHS
Spacing: N/A
Post 1 Length: 3025mm
Base: Type: Combined
Width: 800mm
Length: 1200mm
Depth: 600mm
Volume: 0.864m³
Earth cover: 100mm
Binding layer: 150mm


DIAG 965 & 966 END OF CYCLE ROUTE SIGN AND POST DETAILS
SCALE 1:20



Sign Reference	Width (mm)	Height (mm)	Background	Border	Legend
965	450	450	Blue	White	White

Structural Calculation Details

Sign: Reference Sign 1
Width: 450mm, Height: 450mm
Shape: Rectangular
Orientation: Facing front
Mounted on post: 1
Mounting height: 1500mm, at post
Post: 1
Type: 76.1 x 32 CHS
Spacing: N/A
Post 1 Length: 3025mm
Base: Type: Combined
Width: 800mm
Length: 1200mm
Depth: 600mm
Volume: 0.864m³
Earth cover: 100mm
Binding layer: 150mm

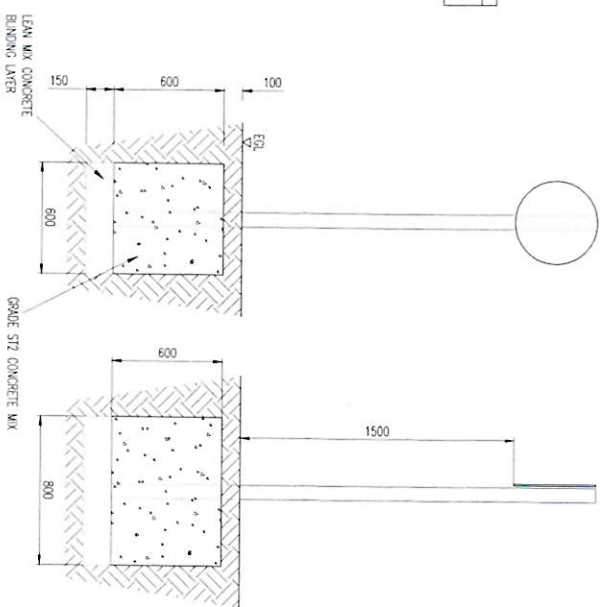

Sign Reference	Width (mm)	Height (mm)	Background	Border	Legend
602	1020	900	White	Red	Black

Sign Reference	Width (mm)	Height (mm)	Background	Border	Legend
602	1020	900	White	Red	Black




Sign Reference	Width (mm)	Height (mm)	Background	Border	Legend
400 yds	991	375	White	Black	Black

Structural Calculation Details

Sign: Reference Sign 1
Width: 991mm, Height: 375mm
Shape: Rectangular
Orientation: Facing front
Mounted on post: 1
Mounting height: 1500mm, at post
Post: 1
Type: 76.1 x 32 CHS
Spacing: N/A
Post 1 Length: 3025mm
Base: Type: Combined
Width: 800mm
Length: 1200mm
Depth: 600mm
Volume: 0.864m³
Earth cover: 100mm
Binding layer: 150mm

Sign: Reference Sign 1
Width: 991mm, Height: 375mm
Shape: Rectangular
Orientation: Facing front
Mounted on post: 1
Mounting height: 1500mm, at post
Post: 1
Type: 76.1 x 32 CHS
Spacing: N/A
Post 1 Length: 3025mm
Base: Type: Combined
Width: 800mm
Length: 1200mm
Depth: 600mm
Volume: 0.864m³
Earth cover: 100mm
Binding layer: 150mm

DIAG 602 GIVE WAY & 531.1A SIGN AND POST DETAILS
SCALE 1:20

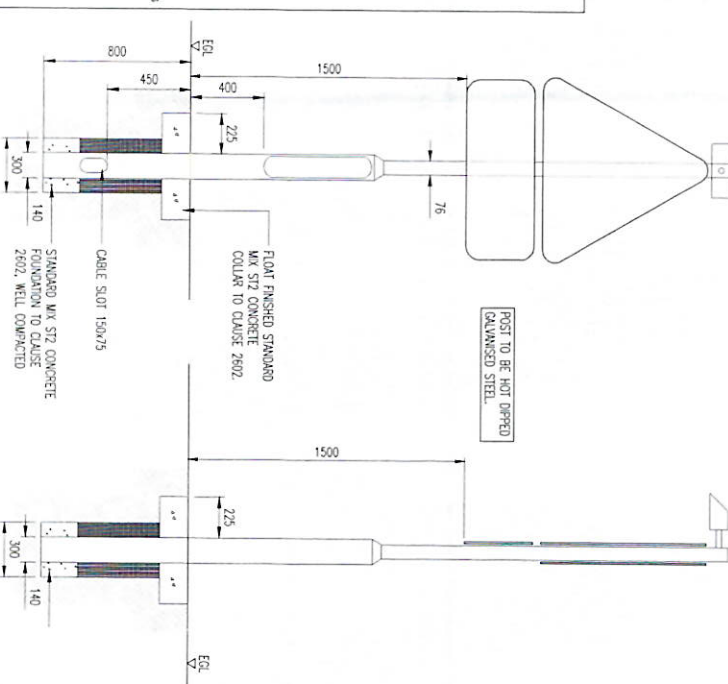

Sign Reference	Width (mm)	Height (mm)	Background	Border	Legend
670	400	400	White	Red	Black

Structural Calculation Details

Sign: Reference Sign 1
Width: 400mm, Height: 400mm
Shape: Rectangular
Orientation: Facing front
Mounted on post: 1
Mounting height: 1500mm, at post
Post: 1
Type: 76.1 x 32 CHS
Spacing: N/A
Post 1 Length: 3025mm
Base: Type: Combined
Width: 800mm
Length: 1200mm
Depth: 600mm
Volume: 0.864m³
Earth cover: 100mm
Binding layer: 150mm

DIAG 670 SPEED LIMIT REPEATER SIGN AND POST DETAILS
SCALE 1:20









Sign Reference	Width (mm)	Height (mm)	Background	Border	Legend
816	480	300	Blue	White	White

Structural Calculation Details

Sign: Reference Sign 1
Width: 480mm, Height: 300mm
Shape: Rectangular
Orientation: Facing front
Mounted on post: 1
Mounting height: 1500mm, at post
Post: 1
Type: 76.1 x 32 CHS
Spacing: N/A
Post 1 Length: 3025mm
Base: Type: Combined
Width: 800mm
Length: 1200mm
Depth: 600mm
Volume: 0.864m³
Earth cover: 100mm
Binding layer: 150mm

DIAG 816 NO THROUGH ROAD SIGN AND POST DETAILS
SCALE 1:20

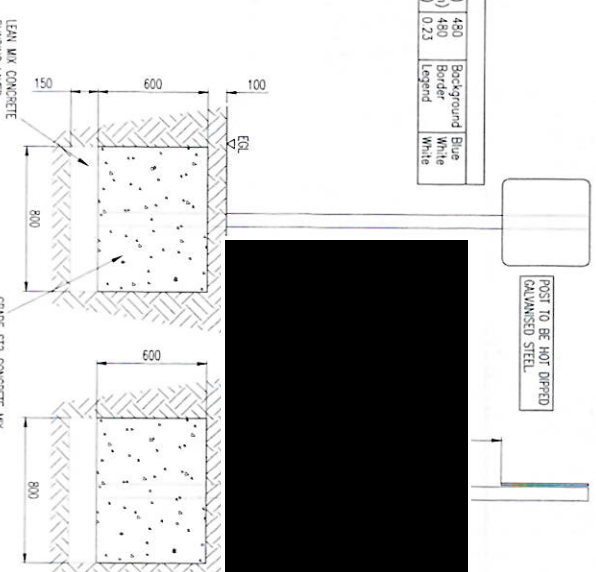

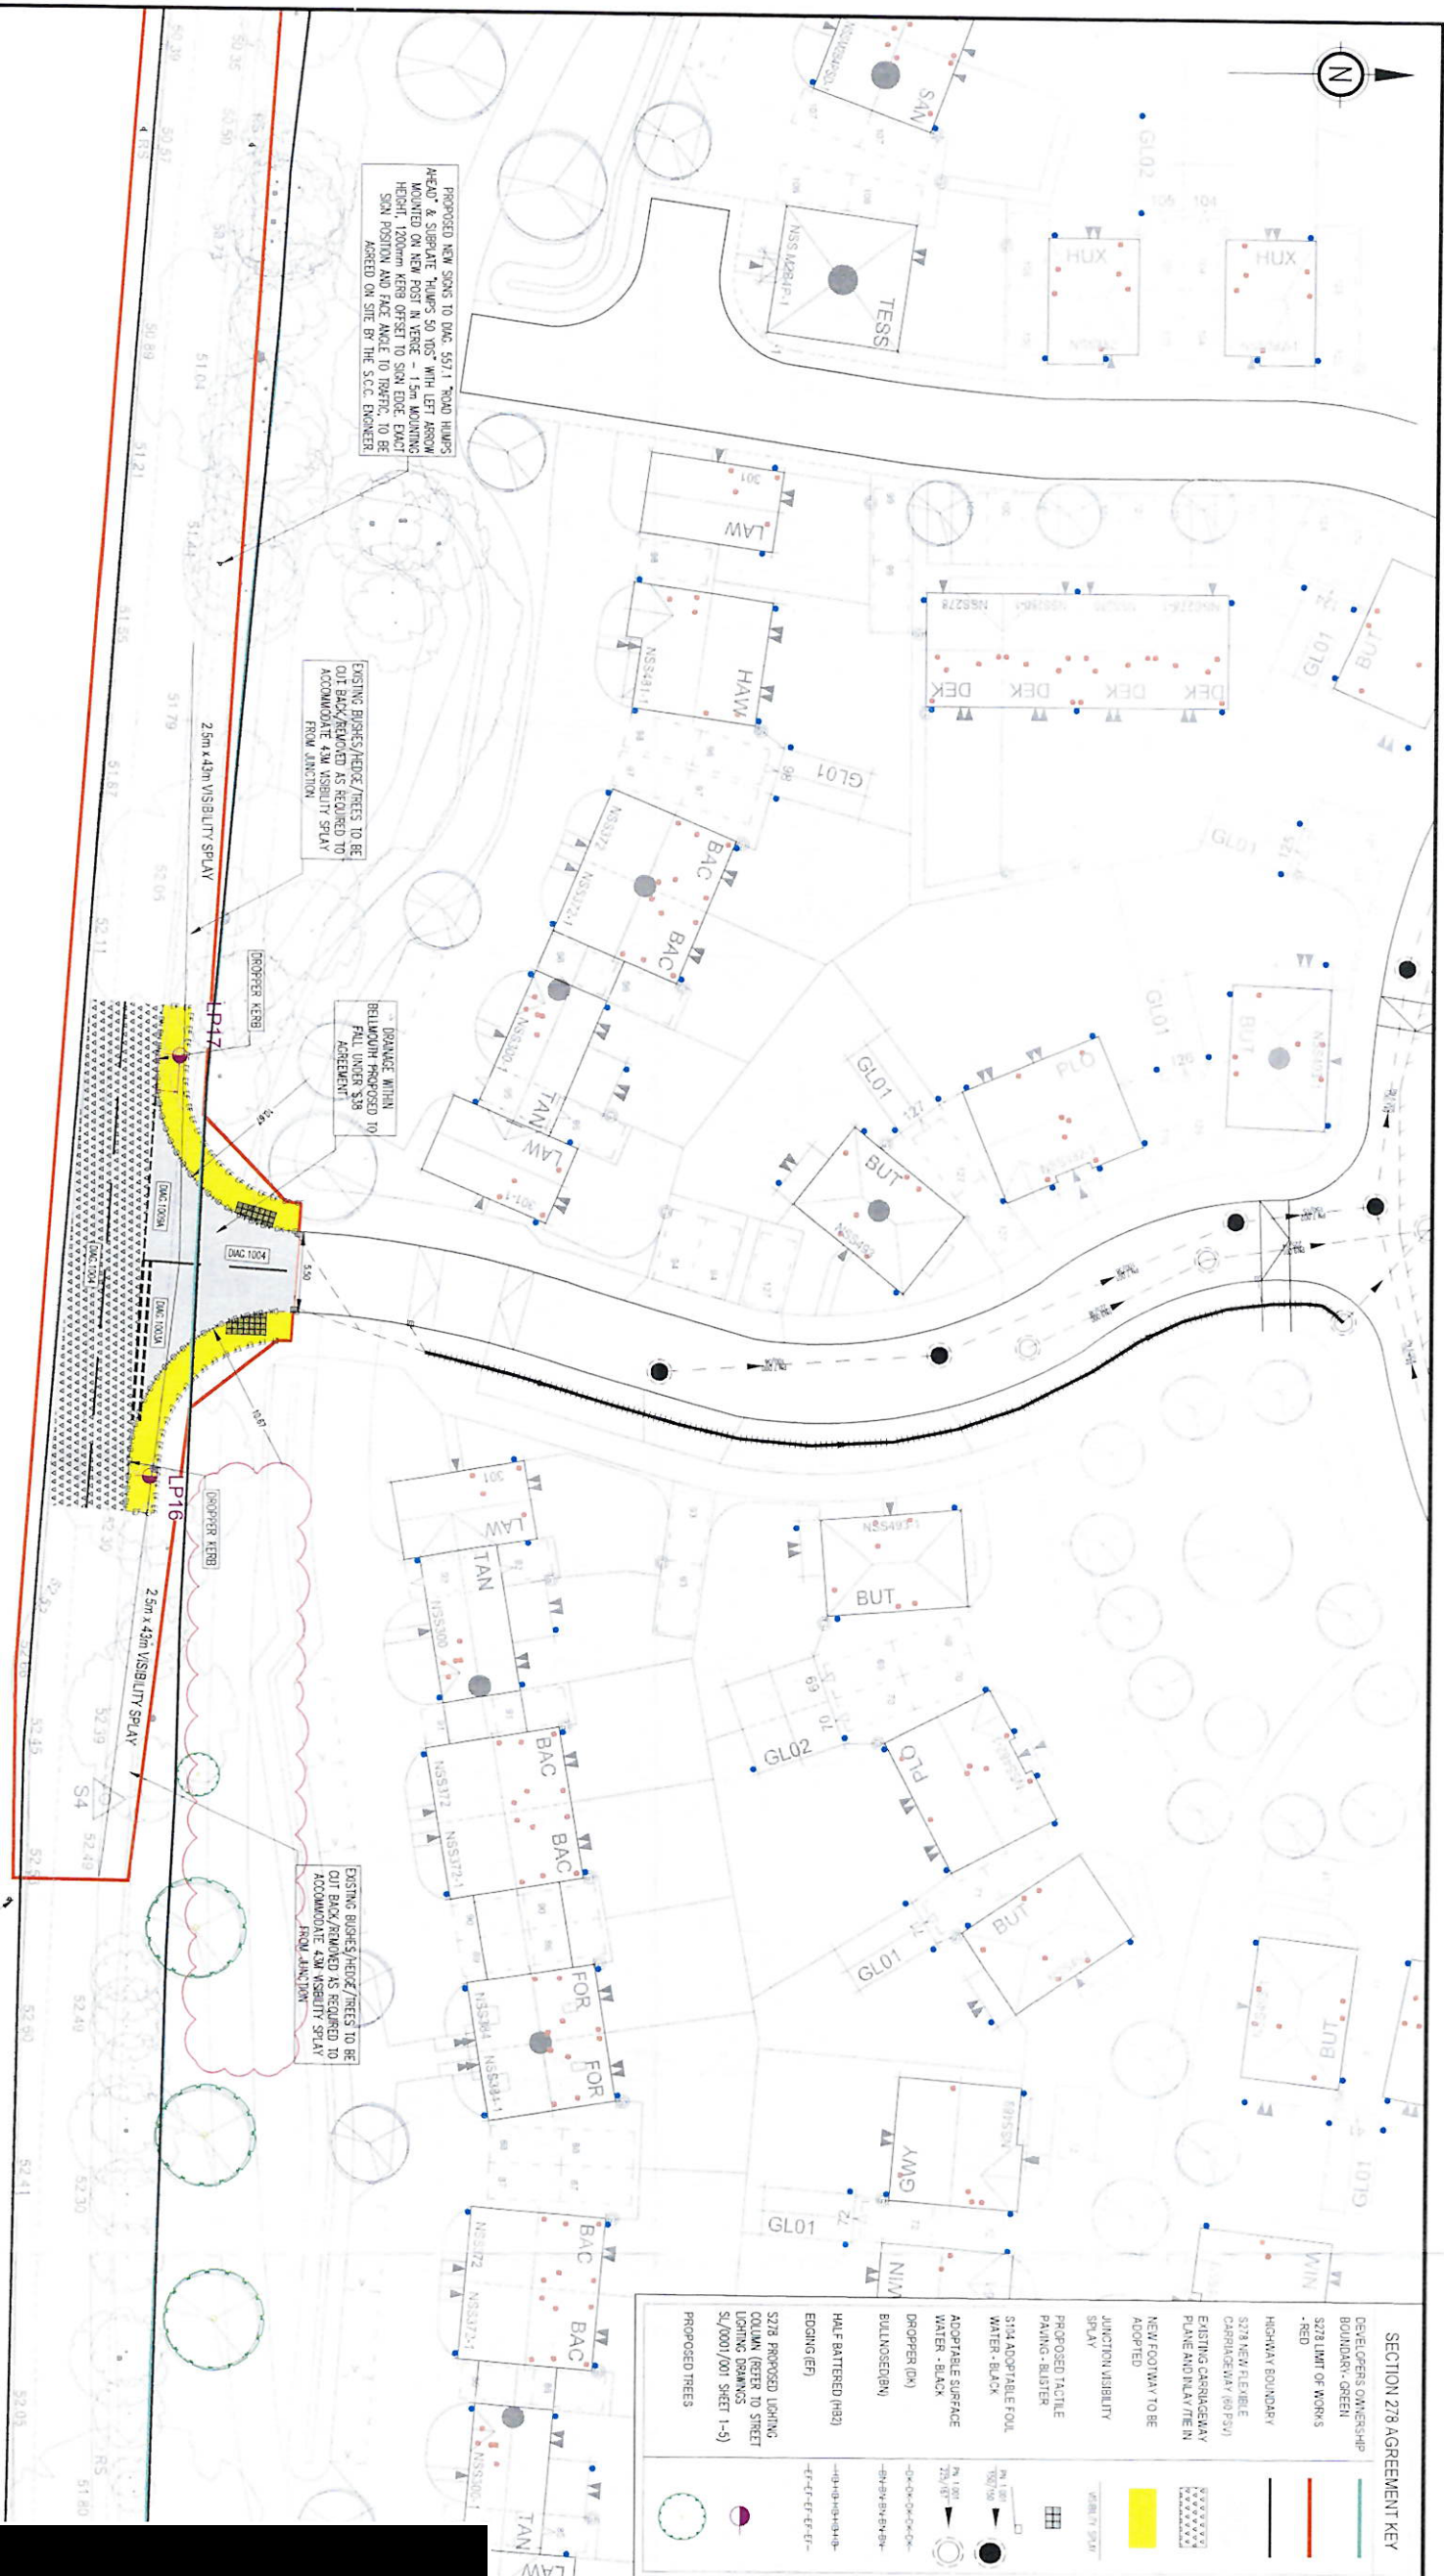

SECTION 278 AGREEMENT KEY

- DEVELOPER'S OWNERSHIP BOUNDARY - GREEN
- S278 LIMIT OF WORKS - RED
- HIGHWAY BOUNDARY - RED
- S278 NEW FLEXIBLE CARRIAGEWAY (60PSY) EXISTING CARRIAGEWAY PLANE AND ALLEYWAY IN NEW FOOTWAY TO BE ADAPTED
- PROPOSED TACTILE PAINTING - BLISTER
- S154 ADAPTABLE POOL WATER - BLACK
- ADAPTABLE SURFACE WATER - BLACK
- DROPPER (DN) BULLDOSE/ENBY
- HAIR BATTERED (H2) EXISTING (EF)
- S278 PROPOSED LIGHTING COLUMN (REFER TO STREET LIGHTING DRAWINGS S/L0001/001 SHEET 1-5)
- PROPOSED TREES

- GENERAL
1. DO NOT SCALE THIS DRAWING. ALL DIMENSIONS ARE IN METRES UNLESS OTHERWISE NOTED. ANY DISCREPANCIES ARE TO BE RECORDED AND REPORTED TO THE ENGINEER IMMEDIATELY.
 2. THIS DRAWING IS TO BE READ IN CONJUNCTION WITH ALL OTHER ENGINEER'S AND ARCHITECT'S DRAWINGS AND THE SPECIFICATION.
 3. ALL WORK IS TO BE TO THE SATISFACTION OF THE ENGINEER AND LOCAL AUTHORITY BUILDING CONTROL.
 4. THE CONTRACTOR IS RESPONSIBLE FOR AND MUST TAKE ALL NECESSARY PRECAUTIONS TO ENSURE THE STABILITY OF THE WORKS AT ALL TIMES DURING CONSTRUCTION.
 5. ALL WORKMANSHIP AND MATERIALS ARE TO BE TO CURRENT BRITISH STANDARDS.
 6. ALL SERVICES ARE TO BE LOCATED AND PROTECTED AS NECESSARY PRIOR TO THE COMMENCEMENT OF THE WORKS.
 7. ANY EXISTING DETAILS WHICH ARE SHOWN ON THIS DRAWING ARE FOR GUIDANCE ONLY AND ARE TO BE CHECKED ON SITE BY THE CONTRACTOR. ANY VARIATIONS ARE TO BE RECORDED AND REPORTED TO THE ENGINEER IMMEDIATELY.
 8. ALL HIGHWAY WORKS ARE TO BE IN ACCORDANCE WITH THE LOCAL AUTHORITY'S DESIGN GUIDE AND SPECIFICATION.
 9. PRIOR TO THE OCCUPATION OF THE FIRST OPENING STREET LIGHTS SHALL BE ERRECTED IN ACCORDANCE WITH THE HIGHWAY AUTHORITY AND TO THE WORKING AGREED WITH THE PLANNING AUTHORITY.
 10. DURING CONSTRUCTION WORKS ON SITE, ALL ROADS AND FOOTPATHS ARE TO BE KEPT OPEN AND KEPT CLEAR OF OBSTRUCTIONS. THIS IS TO INCLUDE EXISTING HIGHWAYS AS APPROPRIATE TO ENSURE SAFE PASSAGE OF ALL ROAD USERS.
 11. PROVISION SHALL BE MADE FOR THE INSTALLATION OF ALL LAMP SERVICES INCLUDING DICTING PRIOR TO THE LAMPING OF THE ROAD BASE COURSE.
 12. ALL ROAD WORKS AND SONS ARE TO BE IN ACCORDANCE WITH THE TRAFFIC SONS REGULATIONS AND DIRECTIONS 2016.

FOR ALL STREET LIGHTING WORKS PLEASE REFER TO THE COUNTY COUNCIL APPROVED STREET LIGHTING DESIGN DRAWINGS.

EXISTING UTILITIES AFFECTED BY THE WORKS TO BE PROTECTED/NOTED IN ACCORDANCE WITH THE REQUIREMENTS AND APPROVAL OF THE RELEVANT STATUTORY AUTHORITIES. LOCATION OF EXISTING UNDERGROUND UTILITY SERVICES TO BE CONFIRMED.

CHECK ALL EXISTING ROAD SONS ARE SUFFICIENT SET BACK FROM ROAD EDGE AND/OR BASED IN HEIGHT FOR RECEPTION/CUTOUT

Unit 15 Greenwood Court, Salford City, Salford, Greater Manchester M6 6PU
Tel: 0161 245024 — www.ingent.co.uk — email: info@ingent.co.uk

PRELIMINARY

Project: BEYTON ROAD, THURSTON, SUFFOLK

Drawing Title: S278 WORKS SOUTHERN ACCESS GENERAL ARRANGEMENT




Client:	BLOOR HOMES	Date:	APRIL 2023
Drawn:	KLK	Checked:	KK
Approved:	KK	Approved:	KK

Scale: 1:250




Project No: PA590-EN

Drawing No & Revision: 340



Size: A1



DIAG 557.1 (600mm) RAMPS AHEAD AND SUB-PLATE (LEFT OR RIGHT AS REQUIRED)
SIGN AND POST DETAILS
SCALE 1:20

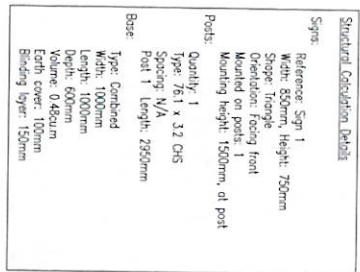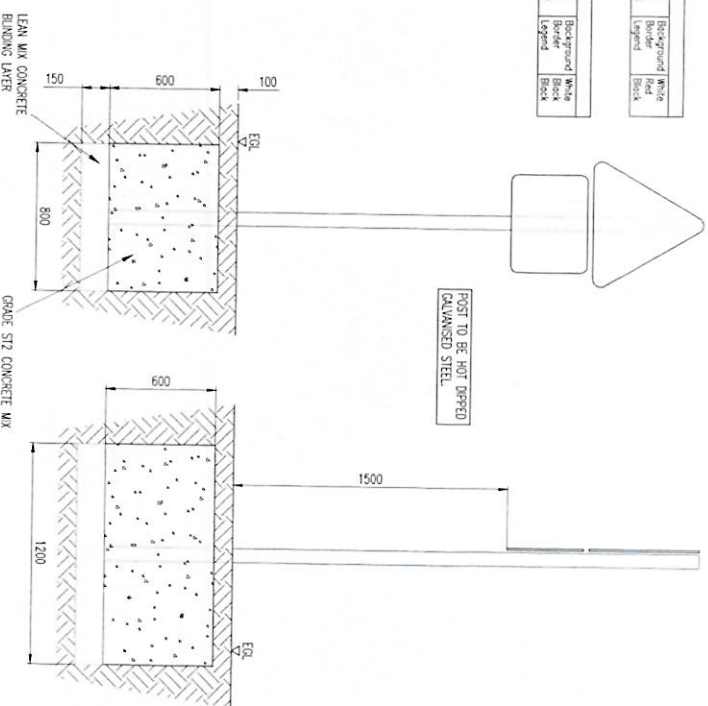

DIAG 512 BEND AHEAD SIGN AND POST DETAILS (LEFT OR RIGHT AS REQUIRED)
SCALE 1:20

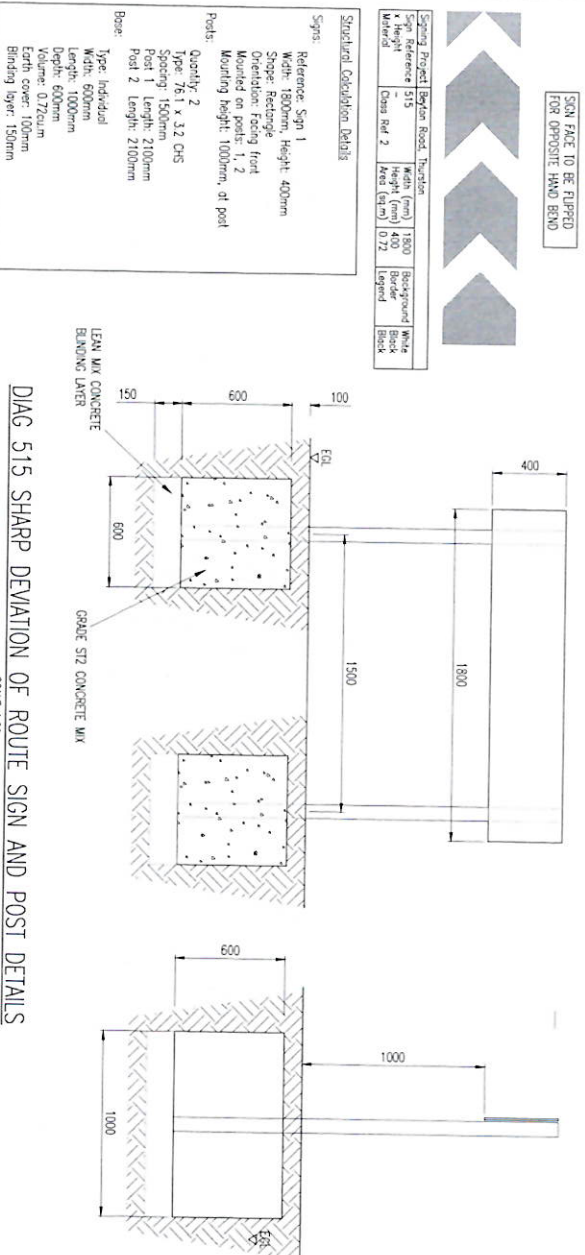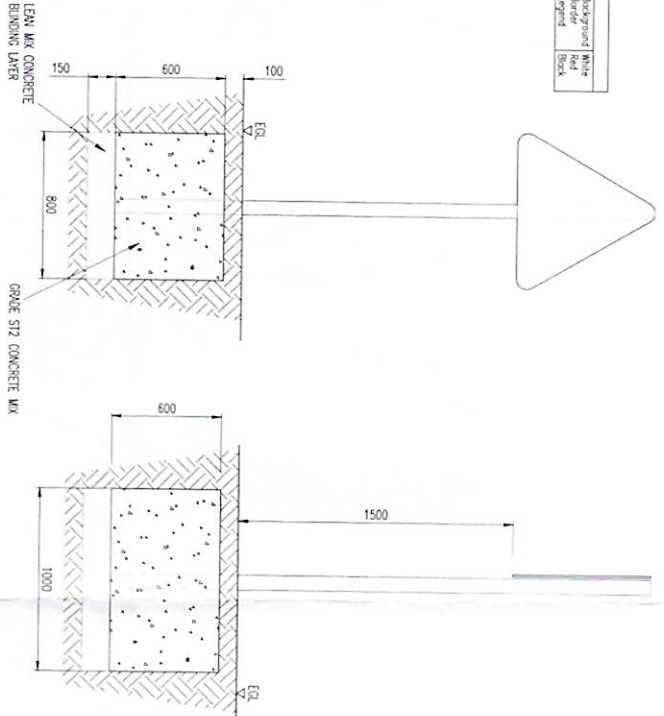

DIAG 515 SHARP DEVIATION OF ROUTE SIGN AND POST DETAILS
SCALE 1:20

- GENERAL NOTES:
1. ALL DIMENSIONS ARE IN MILLIMETERS UNLESS OTHERWISE NOTED. ANY DISCREPANCIES ARE TO BE REPORTED AND RESOLVED IMMEDIATELY.
 2. THIS DRAWING IS TO BE READ IN CONJUNCTION WITH ALL OTHER ENGINEERS AND ARCHITECTS DRAWINGS AND THE SPECIFICATION.
 3. ALL WORK IS TO BE TO THE SATISFACTION OF THE ENGINEER AND SUFFOLK COUNTY COUNCIL HIGHWAYS DEPARTMENT.
 4. THE CONTRACTOR IS RESPONSIBLE FOR AND MUST TAKE ALL NECESSARY PRECAUTIONS TO ENSURE THE SAFETY OF THE WORKS AT ALL TIMES DURING CONSTRUCTION.
 5. ALL WORKMANSHIP AND MATERIALS ARE TO BE TO CURRENT BRITISH STANDARDS.
 6. ALL SERVICES ARE TO BE LOCATED AND PROTECTED AS NECESSARY BY THE CONTRACTOR PRIOR TO THE COMMENCEMENT OF THE WORKS.
 7. ANY EXISTING DETAILS WHICH ARE SHOWN ON THIS DRAWING ARE FOR GUIDANCE ONLY AND ARE TO BE CHECKED ON SITE BY THE CONTRACTOR. ANY VARIATIONS ARE TO BE REPORTED AND REPORTED TO THE ENGINEER IMMEDIATELY.
 8. ALL HIGHWAY WORKS ARE TO BE IN ACCORDANCE WITH THE LOCAL AUTHORITY'S DESIGN GUIDE AND SPECIFICATION.
 9. PRIOR TO THE OCCUPATION OF THE FIRST DWELLING, STREET NAMEPLATES SHALL BE INSTALLED IN ACCORDANCE WITH THE HIGHWAY AUTHORITY AND TO THE WORKING AGREED WITH THE PLANNING AUTHORITY.
 10. DURING CONSTRUCTION WORKS ON SITE, ALL ROADS AND FOOTPATHS ARE TO BE KEPT CLEAR OF OBSTRUCTIONS. THIS IS TO INCLUDE EXISTING HIGHWAYS AS APPROPRIATE TO ENSURE SAFE PASSAGE OF ALL ROAD USERS.
 11. PROVISION SHALL BE MADE FOR THE INSTALLATION OF ALL WORKS SERVICES INCLUDING DITCHING PRIOR TO THE DRAINING OF THE ROAD BASE COURSE.
 12. ALL ROAD WORKS AND SIGNS ARE TO BE IN ACCORDANCE WITH THE TRAFFIC SIGNS REGULATIONS AND DIRECTIONS 2016.

INGENT
CONSULTING ENGINEERS
Unit 15 Greenwood Court, Snyper Way, Bury St Edmunds, IP37 7GJ
Tel: 01284 245074 — www.ingent.co.uk — email: info@ingent.co.uk

PRELIMINARY

Project: **BETON ROAD, THUNSTON, SUFFOLK**

Drawing Title: **S278 WORKS SOUTH ACCESS & MOUNT ROAD STANDARD CONSTRUCTION DETAILS SHEET 02 OF 02**


Client	Drawn	Checked	Approved	Date
BLOOR HOMES	KLK	KLK	KLK	APRIL 2023

Scale: 1:20

Project No: PAS50-EN-343

Drawing No & Revision: 343

Size: A1

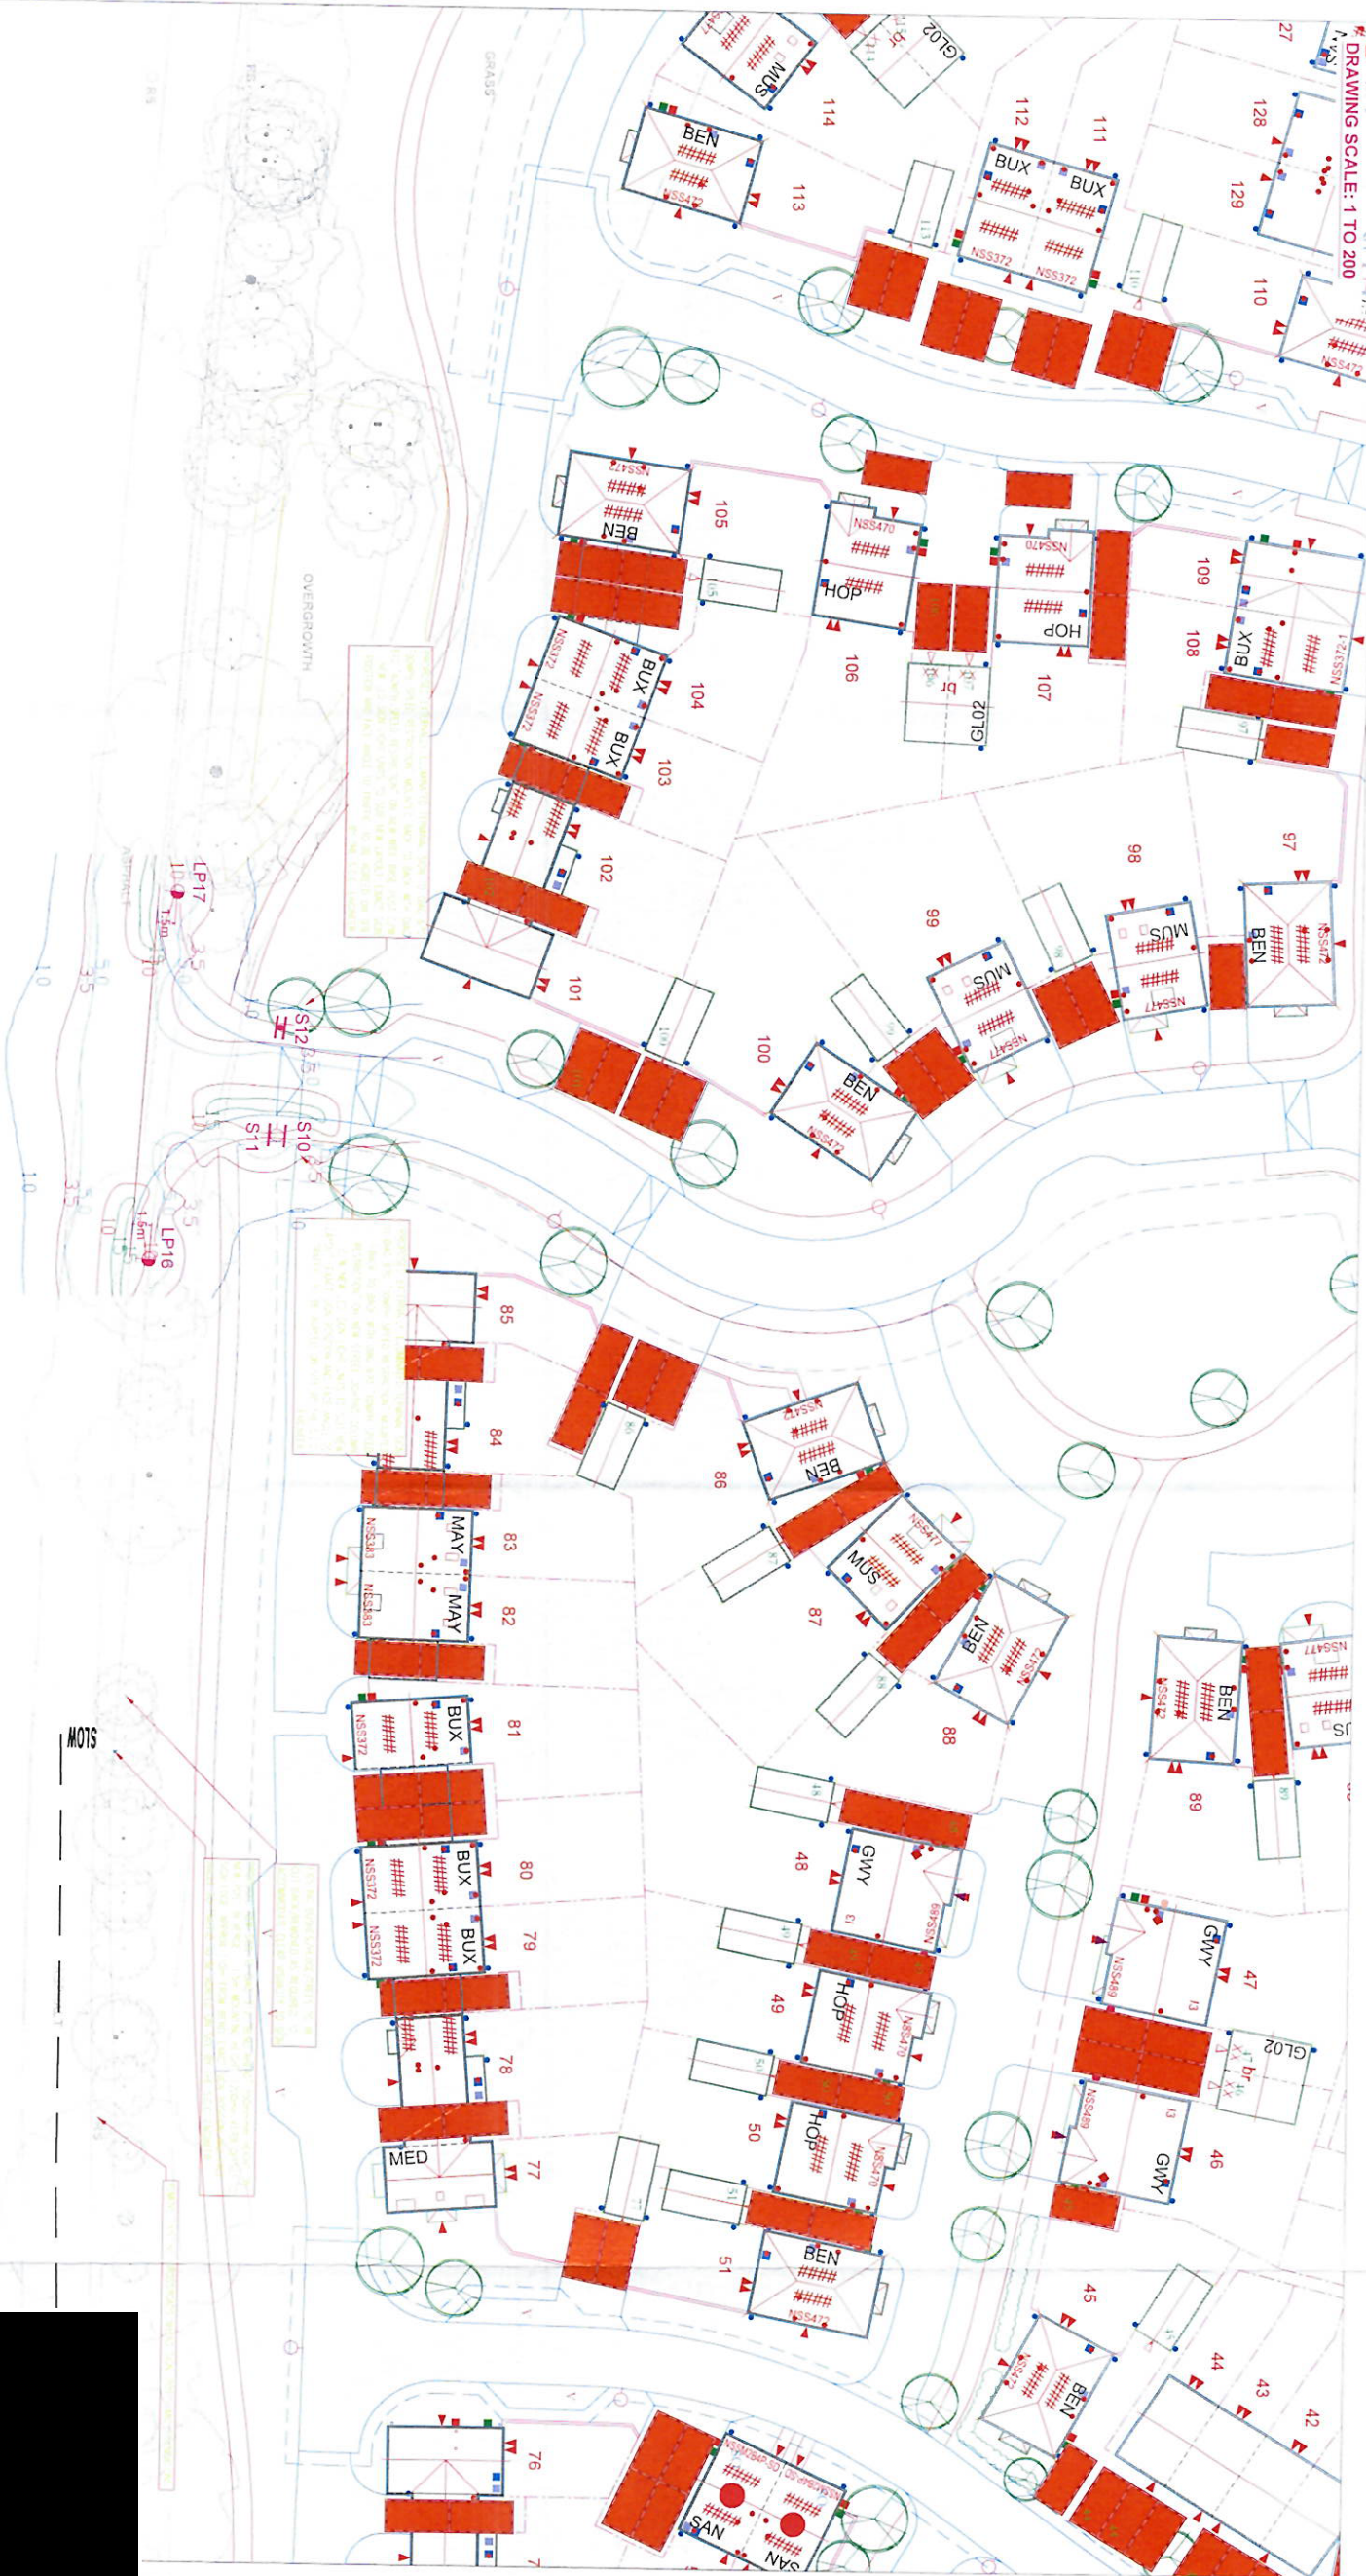

STREET LIGHTING LEGEND:-

- - Use lighting columns to be installed as part of Section 30.000, Column Work.

REPLACE EXISTING LIGHTING COLUMN.

- [illegible]

REPLACE EXISTING LANTERNS

- [illegible]

NEW LIGHTING COLUMNS AND LANTERNS

- [illegible]

NEW ZEBRA CROSSING LIGHTING UNITS.

- [illegible]

NEW ILLUMINATED SIGNAGE

- [illegible]

STREET LIGHTING
DESIGN
APPROVED
BY SUFFOLK COUNTY
COUNCIL'S
STREET LIGHTING
DEPARTMENT

REVISED:-
SIGNED:-
DATED:- 20th November 2023



REPLACE EXISTING LIGHTING COLUMN

[illegible]

NEW LIGHTING COLUMNS AND LANTERNS

SAFETY AND PROTECT YOUR INVESTMENT IN STEEL LIGHTING COLLECTIVE WITH SPECIAL 12' AND 20' AND TWO PORT TOP AND BOTTOM PROTECT WITH 2.25" INCH POWER VENTING AND 10" INCH VENTING WITH 1.5" INCH SETTING COATS AND 10" INCH ELECTRICALLY CONTROLLED THERMOSTAT. NEW VENTING SYSTEMS WITH PROTECT. CONCRETE THERMOSTAT AND CHAIRS ELECTRICITY IS BUILT IN. NEW VENTING SYSTEMS AND CHAIRS ELECTRICITY IS BUILT IN. NEW VENTING SYSTEMS AND CHAIRS ELECTRICITY IS BUILT IN.

SAFETY AND NOT ALL. THE NEW GALVANNEED TUBULAR STEEL, USED COMPLETELY WITH GLASS FLUORIDE ROOF AND TWO POST TOP MOUNTED PHOTO MOUNTED 2.5 KW PHOTO POWER SYSTEMS IN A NEW

COLUMBIAN SUEY FACTORY FRIED 7 PM NEWS SOCKET. SPART PRISONERS
#TILDEBA TELICELL UNIT AND CHARGES DISOBEY LA DOUBLE FOUR
POLICE IN BANG OF COLUMBIA
NEW COLUMBIA TO HAVE LONG STATISTOR MANS ELECTRICITY BY JUNE

NEW ZEBRA CROSSING LIGHTING UNITS.

NEW ILLUMINATED SIGNAGE.

NEW ILLUMINATED SIGNAGE

[illegible]

100
